


Louisiana Transportation Infrastructure Fund

December 2025



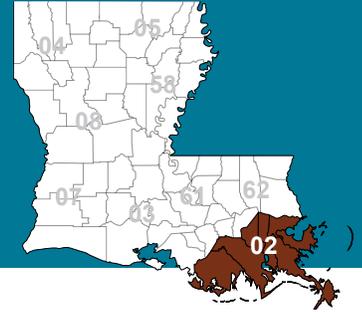

Milling operations on LA 18

Construction Projects

- **LA 18/18S (Jefferson)** - A majority of the month was devoted to milling operations along these highways with work occurring on both northbound and southbound lanes, as well as turnouts at local road intersections. Minor repairs and adjustments were also made to drains/manholes affected by milling operations along the route. Cold weather prevented asphalt from being applied until the mid to latter part of the month when temperatures were within acceptable range. DOTD has made \$326,426.35 in payments thus far on this project that is currently projected to cost \$923,807.85.
- **LA 20 drainage improvements (Lafourche)** - Kelly Industries LLC was awarded a drainage project totaling \$44,341.00 in Lafourche Parish. Work was completed along LA 20 to shape and grub an existing ditch to allow positive drain flow. Long reach excavators were used for grubbing under the adjacent bridge to improve overall drainage in the area.

Guardrail Retainer Contract

Several guardrail repairs occurred and were invoiced in December. Five guardrail repairs occurred along I-10, three of which were in Orleans Parish and two in Jefferson Parish. A sixth guardrail repair occurred along LA 315 in Terrebonne Parish at the approach of the Dularge Bridge. The cost of these six repairs totaled \$29,155.12, and a grand total of \$98,435.32 has been invoiced for District 02 thus far for the current fiscal year.

Upcoming Projects

- An asphalt pavement patching and markings project along U.S. 61 from LA 50 to Ormond Boulevard in St. Charles Parish was awarded to Barriere Construction in the amount of \$1,196,211.60.
- An asphalt pavement patching and markings project along LA 428 from the Jefferson Parish line to Behrman Place in Orleans Parish was awarded to Barriere Construction in the amount of \$887,693.15.
- An asphalt pavement patching and markings project along LA 308 from Percy Brown Road to Canal Boulevard in Lafourche Parish was awarded to Huey Stockstill Inc. in the amount of \$434,935.00.
- Two additional projects were let for signal repairs and bridge rail repairs and have not yet been awarded. Updates on awarded bids to follow next month.

**DOTD
District 02**

Jefferson
Lafourche
Orleans
Plaquemines
St. Bernard
St. Charles
Terrebonne


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$0.00
- **Contracts:** \$1,362,816.54
- **Equipment/rentals:** \$0.00

Parish and Amount Spent Since July 1, 2025

- **Jefferson:** \$474,634.39
- **Lafourche:** \$44,341.00
- **Orleans:** \$519,920.57
- **Plaquemines:** \$318,495.49
- **St. Bernard:** \$0.00
- **St. Charles:** \$0.00
- **Terrebonne:** \$5,425.09

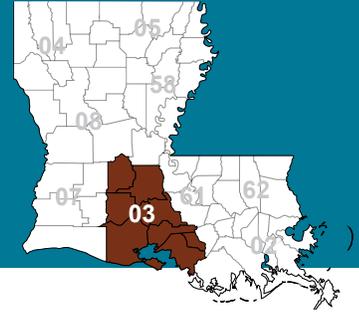

Contracts

- A total of \$20,960.00 was paid toward the District 03 guardrail repair contract for the repair of guardrail located on LA 14 and U.S. 90 in Iberia Parish, LA 35 in Acadia Parish, LA 328 in St. Martin Parish, and U.S. 190 in St. Landry Parish.
- \$15,000.00 of supplemental funding paid toward the new U.S. 190 maintenance mowing contract, which is comprised of six mowing cycles and eight litter collection cycles developed for Acadia, Evangeline, and St. Landry parishes.
- A notice to proceed has been executed for the bridge approach slab undersealing repair project involving designated structures in Acadia, Lafayette, and St. Martin parishes awarded in the amount of \$429,110.00 with an anticipated startup in early January, along with the concrete barrier repair project at locations in Acadia, St. Martin, and St. Landry parishes awarded in the amount of \$511,940.00.
- Other contracts remaining in the developmental stage:
 - Cross drain lining deterioration repair contract required re-advertisement and bids are scheduled to be opened the first week of January.
 - Cross drain replacement contract for LA 13 in St. Landry Parish with a budget of approximately \$250,000.00 has been advertised, with a bid opening date the first week of January.
 - \$21,455.00 has been allocated for the design portion of a high mast lighting retrofit project for the Butte La Rose rest area in St. Martin Parish. The consultant is currently working on the design, with an anticipated two-month time frame for completion.

Materials

- Supplemental funding used to support overlay projects with asphalt, fuel, and other materials:
 - Supplemental funding support of LA 682 overlay project in Iberia Parish this month was \$82,102.80, resulting in a final total expense of \$190,768.59.
- \$2,982.00 of supplemental funding asphalt material starts the roadway shrinkage cracks/pavement faulting repair on LA 82 in Vermilion Parish. This work is anticipated to continue throughout January and February within Vermilion and Iberia parishes on designated areas of LA 82, LA 674, LA 14, and LA 182.
- Supply purchases awaiting final processing:
 - The \$28,940.00 purchase order for the replacement of moveable bridge sewer treatment plants at the Adeline and Humble Canal bridges has been approved. Delivery and installation of new treatment plants anticipated for January.

- The purchase of additional piping to replace culvert located on LA 35 in Acadia Parish.
- A purchase order in the amount of \$219,100.00 was created for the acquisition of spans and caps to facilitate in-house bridge replacements

Equipment:

- A force feed loader is in ordered status with purchase order in the amount of \$383,430.88, and a mechanical street sweeper is in bid status.
- Monthly equipment rental cost for dump trucks, bucket trucks, rollers, sweepers, etc. will resume in January upon contract renewal.

Spending

Spending Category and Amount Spent Since July 1, 2025


- **Materials:** \$473,143.80
- **Contracts:** \$257,414.16
- **Equipment/rentals:** \$303,285.78

Parish and Amount Spent Since July 1, 2025

- **Acadia:** \$117,401.34
- **Evangeline:** \$61,491.00
- **Iberia:** \$336,148.80
- **Lafayette:** \$55,231.16
- **St. Landry:** \$87,034.00
- **St. Martin:** \$75,423.40
- **St. Mary:** \$11,568.00
- **Vermilion:** \$157,270.45

DOTD District 03

Acadia
Evangeline
Iberia
Lafayette
St. Landry
St. Martin
St. Mary
Vermilion

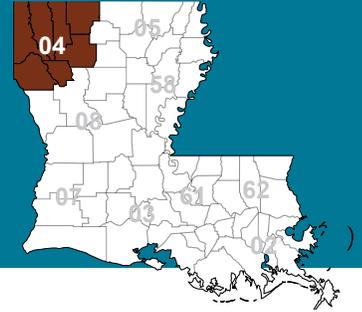

District 04 maintenance crew laying hot mix



U.S. 371 in Red River Parish completed overlay for this section

Hot Mixing in District 04

Maintenance crews in District 04 continued laying down hot mix. The in-house unit and their equipment stayed in Red River Parish, and U.S. 371 was the target of the crew. 1,376.68 tons of asphalt was laid over 1.62 miles. The cost of the materials came to \$151,550.26.

Second Quarter Recap

It has been a busy second quarter for District 04. In October, the district's striping crew striped 195 miles using 57,550 pounds of glass beads and

8,600 gallons of paint. Among the highways that were newly striped are LA 516 and LA 792 in De Soto Parish and LA 175 and LA 765, just to name a few.

The in-house hot mix crew was busy in October and November. In October, U.S. 371 in Webster Parish and U.S. 79 in Claiborne Parish received a fresh coat of hot mix. A total of 8.9 miles were overlaid with 7,433 tons of material at a cost of \$818,568.87. November saw hot mix jobs picking back up in Claiborne Parish and then continuing into Red River Parish. Claiborne Parish's LA 9 received 3.28 miles of new overlay, and the crew then moved to Red River Parish to put fresh asphalt on portions of U.S. 71, U.S. 84, and LA 480. In total, 4.49 miles were overlaid with 5,037.36 tons of material at a cost of \$436,920.86.

DOTD District 04

Bienville
Bossier
Caddo
Claiborne
DeSoto
Red River
Webster


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$3,074,402.36
- **Contracts:** \$692,414.92
- **Equipment/rentals:** \$506.00

Parish and Amount Spent Since July 1, 2025

- **Bienville:** \$922,061.27
- **Bossier:** \$34,569.26
- **Caddo:** \$712,131.78
- **Claiborne:** \$876,444.06
- **DeSoto:** \$7,011.98
- **Red River:** \$277,352.88
- **Webster:** \$937,752.05

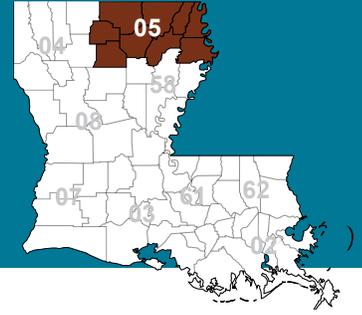

LA 4 completion of cross drain in Jackson Parish

Emergency Cross Drain Replacement

A damaged cross drain in Jackson Parish called for an emergency road closure on LA 4. The closure was necessary to allow for the replacement of a cross drain pipe that failed and was causing a deflection of the roadway. The cross drain was replaced with three 30"x20' storm drain pipes. The pipe was replaced using in-house forces under supplemental funding. Total cost of storm pipe was \$3,744.00.

Upcoming Projects to Begin in New Year

- Districtwide signal crew begins installing new radar detection systems at multiple locations within the district.
- New contract to be let in mid-January. Concrete patching on U.S. 167 will begin in Lincoln and continue through Union and Jackson parishes.

Asphalt Year-Ending Totals for the District

- **Madison**
 - Asphalt tons: 1774.81
 - Miles paved: 3.073
 - Cost: \$199,666.13
- **West Carroll**
 - Asphalt tons: 1799.69
 - Miles paved: 3.69
 - Cost: \$196,462.78

- **East Carroll**

- Asphalt tons: 649.20
- Miles paved: 3.216
- Cost: \$83,035.70

- **Morehouse**

- Asphalt tons: 24.18
- Miles paved: 20.47
- Cost: \$28,001.68

Spending

Spending Category and Amount Spent Since July 1, 2025


- **Materials:** \$569,918.41
- **Contracts:** \$149,520.44
- **Equipment/rentals:** \$0.00

Parish and Amount Spent Since July 1, 2025

- **East Carroll:** \$83,419.88
- **Jackson:** \$42,503.46
- **Lincoln:** \$35,864.68
- **Madison:** \$218,256.27
- **Morehouse:** \$36,612.87
- **Ouachita:** \$63,835.10
- **Richland:** \$37,291.20
- **Union:** \$5,190.48
- **West Carroll:** \$196,464.91

DOTD District 05

East/West Carroll
Jackson
Lincoln
Madison
Morehouse
Ouachita
Richland
Union

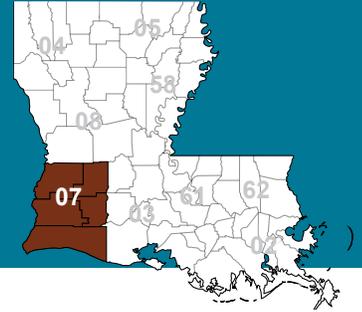

Area of cleared trees along I-10 near Jennings

Contracted Work

In December, Burns Maintenance Group removed trees in the DOTD right-of-way on I-10 eastbound between LA 102 and LA 97 in Jennings. During the last snow and ice event, this section of the interstate was closed due to ice formation. Shading of the roadway impeded thawing in daytime hours. The trees were removed to mitigate prolonged ice formation during winter weather and to enhance traveler safety by clearing obstructions from the right-of-way.

Approximately seven acres of trees were removed for a contract cost of \$221,750. Supplemental funding was used for this project.

Contracted mowing and litter collection acreage was increased in Allen Parish. \$12,122 in supplemental funds were used to pay Specialty Services to mow and pick up litter on U.S. 165 from north of the city of Oakdale to the Rapides Parish line.

Traffic Signal Upgrades

This month, four signal intersections received ITS Plus video detection upgrades. Two signals were located in Jefferson Davis on LA 99 and U.S. 90, and two signals were located on LA 385 (Ryan Street) in Calcasieu. This completes the 10 signals planned for detection upgrade. A total of \$43,800 in supplemental funds were used to purchase materials for this project.

Maintenance Materials

In December, Calcasieu Parish maintenance used 26.84 tons of hot mix asphalt to patch a location on I-210 frontage and a second location on U.S. 90 in Lake Charles. Supplemental funds spent: \$3,006.

Jennings maintenance used 18.05 tons to patch two locations on LA 26 in Jennings. Supplemental funds totaling \$2,022 were spent on materials for this job.

District 07 sign crews replaced 108 signs and 139 posts this month. Materials total: \$2,393.

District striping crew striped 16.3 line miles of pavement. Materials used were 2,600 pounds of glass pavement marking beads and 427 gallons of stock paint. Supplemental funding cost: \$2,340.

Supplemental funds totaling \$4,249 were used to rent street sweepers. These sweepers were used to clean multiple bridges in the district prior to in-house crews applying Pavix to the bridge deck. Pavix application is intended to help with the removal of snow and ice during winter weather events. This product has an estimated lifespan of up to 15 years.

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$962,728.23
- **Contracts:** \$350,384.76
- **Equipment/rentals:** \$28,854.21

Parish and Amount Spent Since July 1, 2025


- **Allen:** \$156,532.82
- **Beauregard:** \$100,381.39
- **Calcasieu:** \$288,748.55
- **Cameron:** \$275,872.52
- **Jefferson Davis:** \$520,431.92

DOTD District 07

Allen
Beauregard
Calcasieu
Cameron
Jefferson Davis



Supplemental Funds

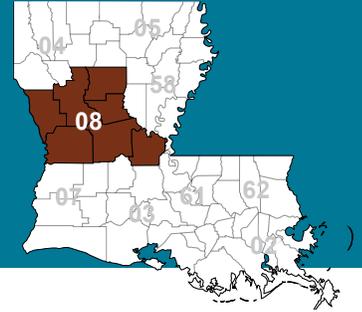

Patch, Mill, and Overlay Projects

In December, in-house crews laid 1,948.15 tons of hot mix asphalt on LA 392 in Vernon Parish at a cost of \$198,711.30. Madden Contracting Co., LLC completed the mill and overlay project on LA 120 that began in early November. This project originally bid for \$705,541.80, but after an approved change order of \$280,379.65, this project cost \$985,923.45.

Sign Repair/Replacement

In December, in-house crews replaced/repared 88 damaged signs in an effort to maintain roadway safety on LA 6, LA 34, LA 463, LA 488, LA 495, LA 497, U.S. 71, and U.S. 171 in Grant, Natchitoches, Rapides, Sabine, Vernon, and Winn parishes. Sign repair/replacement projects have cost \$1910.42 in December.

Cable Barrier and Guardrail Repair

Supplemental funds are being used to repair damaged cable barrier and guardrail throughout the district in order to ensure roadway safety. In December, two sections of cable barrier were repaired on I-49 by in-house crews in Avoyelles Parish. This repair cost \$292.66. Additionally, two sections of guardrail in Natchitoches Parish and one section of guardrail in Rapides Parish were repaired by a contractor at a cost of \$19,375.00.

Pavement Striping/Raised Pavement Marker Application Projects

District 08 continued using supplemental funds on pavement striping/raised pavement marker improvement projects across the district in December. In-house crews completed projects in Natchitoches and Winn parishes. Unit 771 placed 700 raised pavement markers on LA 495 in Natchitoches Parish. In Winn Parish, crews striped an estimated 9.17 line miles of roadway on LA 34, U.S. 84, and U.S. 167 using 4,000 pounds of glass beads and 250 gallons of paint. Pavement striping and raised pavement marker application projects have cost \$7,124.00 in December.

Wavetronix Detection Systems

District 08 purchased materials with supplemental funds to install Wavetronix Detection Systems throughout the district. In December, in-house crews installed new systems at three traffic signals on U.S. 171 in Vernon Parish. These installations cost \$36,460.00 in supplemental funds.

Mowing/Litter Pickup

\$184,895.86 in supplemental funds has been spent on additional mowing and litter pickup cycles for interstates and U.S. highways throughout the

district. This includes \$36,652.00 on I-49 in Avoyelles Parish, \$47,700.00 on U.S. 165 and U.S. 167 in Grant Parish, \$38,271.93 on U.S. 71 in Sabine Parish, \$38,271.93 on U.S. 71 in Vernon Parish, and \$24,000.00 on U.S. 167 in Winn Parish. Additionally, \$80,131.25 was spent for additional mowing cycles on state routes within municipalities throughout the district.

Fast Facts

- District 08 purchased barricade lights at a cost of \$4,133.80 to be used for roadway safety throughout the district.
- Materials were purchased for bulk storage of salt in preparation for winter weather response. Materials cost \$4,466.75.

Spending

Spending Category and Amount Spent Since July 1, 2025


- **Materials:** \$1,210,137.07
- **Contracts:** \$1,872,146.47
- **Equipment/rentals:** \$0.00

Parish and Amount Spent Since July 1, 2025

- **Avoyelles:** \$123,956.34
- **Grant:** \$182,881.88
- **Natchitoches:** \$328,970.26
- **Rapides:** \$475,611.81
- **Sabine:** \$1,104,526.84
- **Vernon:** \$407,095.52
- **Winn:** \$459,240.90

DOTD District 08

Avoyelles
Grant
Natchitoches
Rapides
Sabine
Vernon
Winn

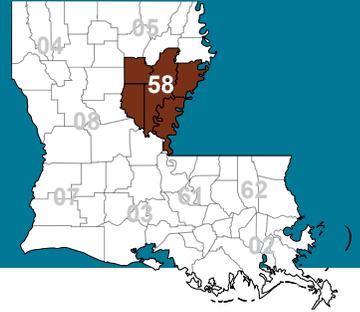

New John Deere 325G

Contracts Let and Ready to Let

A tree removal contract let on December 16 and was awarded to Traffic Commander, LLC for \$999,300.00. The plans project that a total of 172 trees will be removed from the rights-of-way in LaSalle, Catahoula, and Concordia parishes.

Another smaller tree removal contract for Caldwell, Franklin, and Tensas parishes will be let on January 22.

Another microsurfacing contract will be let on February 26. This contract will address LA 130 in Franklin Parish, and its estimated cost will be \$433,000.

Finally, two contracts are ready to be let on January 22 and February 26 to fix damaged areas of U.S. 65 in Tensas Parish. A joint rehab contract will address the composite sections of the road, and its estimated cost is \$713,000. The other, a PCCP contract, is for the sections that are concrete pavement, and its estimated cost is \$484,000.

Equipment

A new John Deere 325G off road loader skid steer was purchased and delivered in December for District 58. This equipment cost \$77,703.75 and will be housed at the Caldwell maintenance office. The former skid steer in Caldwell will be moved to the Tensas maintenance office so that they will have a newer model to use.

Striping Miles in December

Striping was delayed by weather in December and will begin again as the weather allows.

Herbicides

There were no new herbicide applications during December. Applications won't begin again until the spring.

Microsurfacing

The project on U.S. 84 has been winterized and will begin in spring when the weather allows.

Future Projects:

- Signal upgrade on U.S. 425 in Franklin Parish
- Asphalt overlay:
 - U.S. 84 in Concordia
 - LA 124 in Catahoula
 - U.S. 165 in LaSalle
 - LA 4 in Franklin
 - LA 133 in Caldwell
 - LA 605 in Tensas

Spending

Spending Category and Amount Spent Since July 1, 2025


- **Materials:** \$231,007.30
- **Contracts:** \$31,933.70
- **Equipment/rentals:** \$91,502.87

Parish and Amount Spent Since July 1, 2025

- **Caldwell:** \$17,131.85
- **Catahoula:** \$48,843.85
- **Concordia:** \$34,661.42
- **Franklin:** \$171,312.92
- **LaSalle:** \$2,359.89
- **Tensas:** \$235.99

**DOTD
District 58**

Caldwell
Catahoula
Concordia
Franklin
LaSalle
Tensas

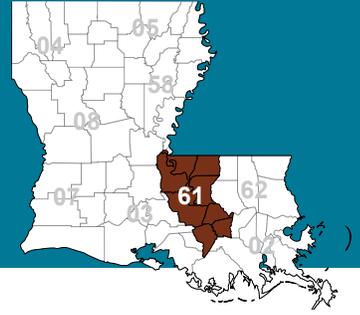

Paving in West Baton Rouge Parish



Guardrail repair before and after

Asphalt and Patching

District paving crews continue the asphalt overlay on U.S. 190 in West Baton Rouge Parish. In December, 2,779 tons of asphalt were put down on the stretch coming off of the Huey P. Long - O.K. Allen Bridge.

Guardrail Repair

Four repairs were made on guardrails in Ascension Parish, three locations on I-10, and one on U.S. 61. One repair was completed on I-12 in East Baton Rouge Parish.

Upcoming Projects:

- Tree removal along LA 409 in East Baton Rouge Parish
- Clearing and grubbing along U.S. 190 in East Baton Rouge Parish
- Drainage structure replacement in Ascension, East and West Baton Rouge, and East Feliciana parishes
- Ditch/pipe/box culvert cleaning in East and West Baton Rouge parishes
- Geo-lined pipe on LA 67 in East Feliciana Parish

DOTD District 61

Ascension
Assumption
East/West Baton Rouge
East/West Feliciana
Iberville
Pointe Coupee
St. James

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$1,291,240.46
- **Contracts:** \$712,911.10
- **Equipment/rentals:** \$0.00

Parish and Amount Spent Since July 1, 2025

- **Ascension:** \$340,062.79
- **Assumption:** \$42,541.11
- **East Baton Rouge:** \$680,058.88
- **East Feliciana:** \$19,367.27
- **Iberville:** \$15,999.45
- **Pointe Coupee:** \$54,177.67
- **St. James:** \$6,934.04
- **West Baton Rouge:** \$417,101.98
- **West Feliciana:** \$140.02



New Graco Grindlazer scarifier



New stop bar on LA 442 in Tangipahoa Parish

Roadway Striping

Pavement markings were added to the railroad crossing on LA-21 in Washington Parish. The yellow and white lines around the islands off the I-55 ramps were refreshed at LaPlace, Manchac, and Ruddock in St. John the Baptist Parish. New pavement striping and stop bars were added to the recent overlay on LA-442 in Tangipahoa Parish.

New Equipment

District 62 traffic operations has received a new Graco Grindlazer gas-powered scarifier, which can be used for pavement marking removal,

surface leveling, and pavement preparation.

Radar Detection

Traffic electricians installed radar detection equipment on LA 3002 in Livingston Parish, and also on I-12 in St. Tammany Parish.

Guardrail Repair

In December, \$45,697.06 was spent on the guardrail repair contract at 17 locations in Livingston, St. John the Baptist, St. Tammany, Tangipahoa, and Washington parishes.

Upcoming Projects:

- Box culvert, cross drain, and ditch cleaning throughout district
- I-10 crack sealing
- Asphalt patching and overlays along several routes
- Tree removal along the interstate right-of-way
- Scrub seals on LA 10, LA 60, and LA 43

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$524,745.99
- **Contracts:** \$497,662.06
- **Equipment/rentals:** \$11,667.00

Parish and Amount Spent Since July 1, 2025

- **Livingston:** \$119,476.56
- **St. Helena:** \$15,968.00
- **St. John the Baptist:** \$101,117.10
- **St. Tammany:** \$224,565.40
- **Tangipahoa:** \$485,985.16
- **Washington:** \$75,295.83

DOTD District 62

Livingston
St. Helena
St. John the Baptist
St. Tammany
Tangipahoa
Washington
