

Louisiana Transportation Infrastructure Fund

November 2025





Cutting patch (left) and breaking it out (right) on LA 18



Grading patch (left) and smoothing/finishing it (right) on LA 18

Construction Projects

LA 23 Emergency Cross Drain

- The second of two emergency cross drain projects in Plaquemines Parish is complete, as the remedial asphalt patching/smoothing work was completed. Final amounts were tallied and adjustments made, which resulted in an overrun of \$37,743.62. The cost of the project, including all change orders and final adjustments, came to a grand total of \$287,430.99 and has been paid in full.

LA 18/18S

- This project to perform asphalt concrete milling and overlay, pavement patching, and pavement markings began in October and continued throughout November. Multiple locations had curb and gutter work done this month, along with pedestrian ramps. Additional patching work was also done in an area where a water line leak occurred. Several change orders were made during November to add concrete curb and gutter, catch basin adjustment, valve and

meter box adjustment, and insurance reimbursement line items. The total cost of these change orders is \$25,216.87, which, when added to the original bid, brings the project total to \$923,807.85. DOTD has paid out \$204,837.88 for the project thus far.

Statewide Renewal Contracts

District 02 Guardrail Retainer Contract

- Three guardrail repairs were performed by contractors in November, all of which were in Jefferson Parish. Two repairs were performed on I-10 westbound at the Louis Armstrong New Orleans International Airport exit, and one repair was performed at northbound Causeway Boulevard at the I-10 east/west split. The total cost of the three repairs was \$11,235.02. The grand total through the month of November for all current fiscal year guardrail repairs is \$68,680.20.

Spending

Spending Category and Amount spent since July 1, 2025


- Materials:** \$0.00
- Contracts:** \$1,167,131.95
- Equipment/rentals:** \$0.00

DOTD District 02

Jefferson
Lafourche
Orleans
Plaquemines
St. Bernard
St. Charles
Terrebonne



Supplemental Funds

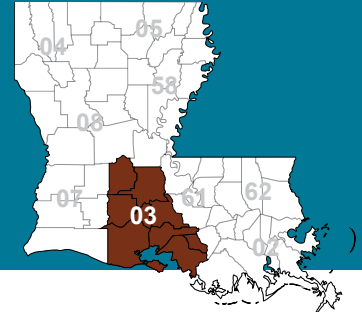

Contracts

- \$20,960.00 was submitted to be paid in early December toward the District 03 guardrail repair contract for the repair of guardrail located on LA 14 in Iberia Parish, LA 35 in Acadia Parish, LA 328 in St. Martin Parish, U.S. 90 in Iberia Parish, and U.S. 190 in St. Landry Parish.
- \$29,000.00 of supplemental funding paid toward the new maintenance mowing contract comprised of six mowing cycles and eight litter collection cycles developed for U.S. 190 throughout Acadia, Evangeline, and St. Landry parishes.
- The bridge approach slab undersealing repair contract involving designated structures in Acadia, Lafayette, and St. Martin parishes was submitted for bid and awarded in the amount of \$429,110.00.
- Other contracts remaining in the developmental stage:
 - Cross drain lining deterioration repair has been advertised and scheduled for bids to be opened on December 4.
 - A cross drain replacement project for LA 13 in St. Landry Parish, with a budget of approximately \$250,000.00, is scheduled to advertise in early December.
 - \$21,455.00 has been allocated for the design portion of a high-mast lighting retrofit project for the Butte La Rose rest area in St. Martin Parish.
 - Thermoplastic roadway striping and marking project.
- The contract for ditch and culvert cleaning efforts along an approximate one-mile span of LA 103 in St. Landry Parish has been cancelled, as the final bid returned over budget and the designated funding was re-signed.
- A contract for the repair of 254 linear feet of concrete bridge barrier across 25 different locations within Acadia, St. Landry, and St. Martin parishes was awarded in the amount of \$511,940.00.
- The Epoxy injection crack repair project on U.S. 90 bridge piles in Iberia Parish completed this month at a total cost of \$68,009.00.

Materials

- Supplemental funding was used to support the following overlay projects with asphalt, fuel, and other materials:
 - **LA 682 in Iberia Parish:** \$86,297.40 (completed project total: \$150,399.00)
 - **LA 3143 in Vermilion Parish:** \$108,665.79 (completed project total: \$669,402.00)
 - **LA 3242 in Iberia Parish:** Scheduled to start in early December.

- \$21,013.20 expensed for material cost to replace a culvert on LA 680 in St. Martin Parish.
- \$51,762.00 of asphalt (488.32 tons) used to repair roadway shrinkage cracks and pavement faulting on LA 92 in Acadia Parish.
- Awaiting final processing:
 - A quote in the amount of \$28,940.00 for the replacement of moveable bridge sewer treatment plants at the Adeline and Humble Canal bridges has been sent to procurement.
 - The purchase of additional piping to replace culvert located on LA 35 in Acadia Parish.
 - A purchase order in the amount of \$219,100.00 was created for the acquisition of spans and caps to facilitate in-house bridge replacements.

Equipment

- Monthly equipment rental cost for dump trucks, bucket trucks, rollers, sweepers, etc.: \$5,502.90
- Purchase orders in the amount of \$823,430.88 have been created for the acquisition of a new sweeper and loader.

Spending


Spending Category and Amount spent since July 1, 2025

- **Materials:** \$387,257.47
- **Contracts:** \$201,234.16 *
- **Equipment/rentals:** \$303,285.78

* The contracts spending summary has been reduced by \$54,717.75, which was the cost of a milling contract for LA 347 in St. Martin Parish completed and reported in September. This cost was reworked into the total project budget and did not require the support of supplemental funding.

DOTD District 03

Acadia
Evangeline
Iberia
Lafayette
St. Landry
St. Martin
St. Mary
Vermilion

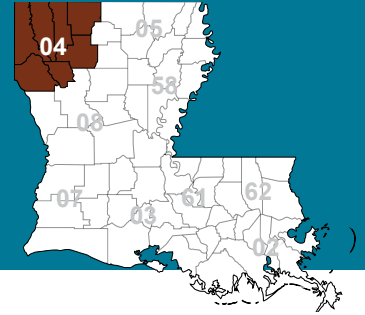

DOTD District 04

Bienville
Bossier
Caddo
Claiborne
DeSoto
Red River
Webster



LA 9 with fresh hot mix in Claiborne Parish

With supplemental funding from the state legislature, \$692,414.92 will be spent on this section of highway. The work will be provided by a private contractor, Progressive Construction Co., LLC.

Webster and Red River Parishes Overlay

District 04 in-house maintenance crews continued the hot mix train. Hot mixing on LA 9 picked up again. 6,384.75 tons of hot mix was laid on 5.83 miles of highway.

The maintenance crew then went south to Red River Parish. Sections of U.S. 71 and LA 480 were hot mixed. U.S. 84 also got new hot mix. A total of 1026.02 tons of hot mix was put down for 1.21 miles.

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$2,381,939.93
- **Contracts:** \$692,414.92
- **Equipment/rentals:** \$506.00




Laying hot mix on U.S. 84 in Red River Parish

Roadway Improvements: Overlay and Pavement Projects

Project 4400033230.6 on LA 511 (West 70th Street) Concrete Patching in Caddo Parish

The LA 511 (West 70th Street) project in Caddo Parish is one step closer to being a reality. Under this project, LA 511 between Jewella Road and U.S. 171 will have repairs made to areas of the roadway that are damaged and have broken up.

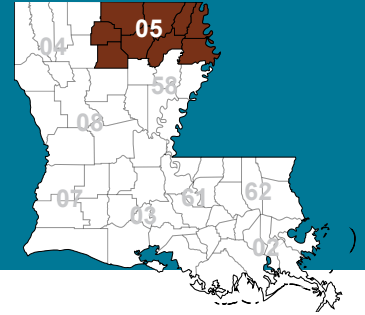

LA 134 drainage replacement in Richland Parish



Timber piles on LA 151 in Lincoln Parish

Asphalt Repairs in District 05

Unit 540 in Morehouse leveled ruts on the roadway on LA 140 and LA 835 to prepare the surface for hot mix application. A total of 9,200 linear feet were resurfaced using a total of 254.18 tons at an estimated cost of \$28,595.27.

Districtwide Unit 710 combined with Unit 590 in East Carroll to repair roadway surfaces on U.S. 65 southbound and northbound. A hot mix overlay job was completed on 0.816 miles of surface using 646.80 tons of hot mix with an estimated cost of \$72,765.00. Unit 590 also completed

overlay jobs on LA 2, LA 580, and U.S. 65, repairing ruts on the road with hot mix totaling 94.71 tons at an estimated cost of \$10,654.88.

Districtwide Unit 710 and Unit 580 worked together in West Carroll for four days to complete a hot mix overlay project to repair roadway surfaces on LA 134. The combined total of miles for the four-day project was 3.69 miles using 1,799.69 tons with an estimated cost of \$196,464.91.

Districtwide Unit 710 and Unit 570 worked together in Madison three days to repair roadway surfaces on LA 134. This hot mix overlay project used 974.79 tons of hot mix costing an estimated \$109,633.98.

DOTD District 05

East/West Carroll
Jackson
Lincoln
Madison
Morehouse
Ouachita
Richland
Union

Drainage Replacement in Richland

A failing cross drain structure on LA 134 in Richland was replaced with 60 feet of 30-inch ADS HP storm drain pipe. The cross drain pipe was purchased under the supplemental funding at a cost of \$3,931.20.

Emergency Bridge Closure in Lincoln Parish


LA 151 in Lincoln Parish required an emergency closure due to decayed timber piles. Four of the timbers used to replace the decaying piles were 25 inch, purchased with supplemental funding.

The total cost of the four 25-inch timbers came to \$2,649.24.

Spending

Spending Category and Amount Spent since July 1, 2025

- **Materials:** \$566,174.17
- **Contracts:** \$149,520.44
- **Equipment/rentals:** \$0.00

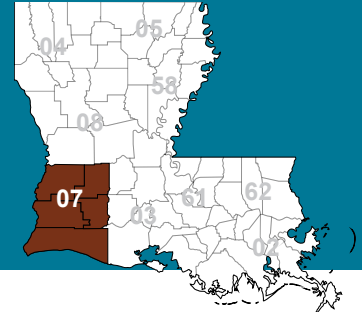

LA 27/82 overlay in Cameron

Overlay on LA 27/82 in Cameron

District asphalt crews overlaid a portion of LA 27 in Cameron. This section of highway in front of the Cameron courthouse would experience periods of inundation due to tidal influences. The road surface was raised approximately four inches to assist with drainage. 1,201.38 tons of hot mix asphalt and 542 gallons of cationic emulsion were applied to the road with a materials supplemental funding cost of \$135,910. An asphalt roller was also rented for \$3,738.

Patching

The Calcasieu maintenance unit patched multiple areas in November. 72.16 tons of hot mix asphalt and 71 gallons of cationic was used at a supplemental funding cost of \$8,269. A location on I-10 over Ruth Street in Sulphur was also patched with polymer concrete resin at a funding cost of \$1,600.

Jefferson Davis maintenance patched locations on LA 26 using 32 tons of hot mix asphalt and 142 gallons of cationic emulsion at a material funding cost of \$3,956.

Movable Bridge Repair

The Grand Lake Pontoon Bridge in Cameron Parish had a new rotary encoder installed. A rotary encoder is a sensor that measures the speed and position of pontoon bridges when opening and closing. Supplemental funding material costs were \$480. Multiple rotary encoder sensors were purchased to be installed on the district's movable pontoon bridges when this type of repair is needed.

Maintenance Materials

Districtwide sign crews installed 363 posts and 137 signs throughout the district in November. Supplemental funds expended on these materials: \$11,102.

A total of 807 gallons of herbicide concentrate was mixed and applied across 855 acres this month districtwide. Supplemental funds totaling \$13,597.35 were used to purchase 250 gallons of the herbicide used.

District 07 striping crews applied 1,032 gallons of paint and 10,200 pounds of glass striping beads to the roadway, covering 54 line miles. Total material costs: \$21,300. They also applied preformed thermoplastic pavement marking symbols on LA 1138-2 (Nelson Road) at I-210 in Lake Charles. New yellow and white plastic paddle delineators were also installed near this location. Materials cost: \$6,399.

Traffic Signal Upgrades

During November, districtwide signal crews worked on upgrading video detection at eight different intersections in Calcasieu Parish. This work took place at two locations on U.S. 90 in Vinton, one intersection at LA 27 in Sulphur, one location each on LA 1138-2 and U.S. 90B, two locations on LA 385 (Ryan Street) in Lake Charles, and one location on LA 378 in Moss Bluff. Current video detection cameras at these intersections were replaced with ITS Plus video detection for a supplemental funding materials cost of \$26,280. More intersection locations are planned for this type of detection upgrade.


Spending

Spending Category and Amount Spent since July 1, 2025

- **Materials:** \$932,474.19
- **Contracts:** \$111,687.50
- **Equipment/rentals:** \$24,604.89

DOTD District 07

Allen
Beauregard
Calcasieu
Cameron
Jefferson Davis

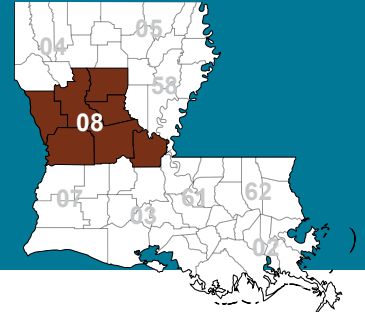

Milling on LA 120 in Sabine Parish

Patch, Mill, and Overlay Projects

In November, in-house crews laid 41.25 tons of hot mix asphalt on the LA 119 bridge over Bayou Pierre in Natchitoches Parish at a cost of \$4,455.00. This project is complete. In Vernon Parish, in-house crews milled and overlaid rutted sections of U.S. 171 near Rosepine using 270.11 tons of hot mix asphalt at a cost of \$27,551.22. This project is also complete. In October, in-house crews completed patching sections of LA 120 in Sabine Parish in preparation for Madden Contracting, Co., LLC to mill and overlay LA 120. The contractor began work on LA 120 in early November and has completed the milling and asphalt portions of the project. The project is expected to be completed in early December, with only permanent striping remaining.

Mowing/Litter Pickup

Supplemental funds are being used for additional mowing and litter pickup contract cycles in Avoyelles, Natchitoches, and Rapides parishes. In Avoyelles Parish, \$30,607.89 was expended on I-49. In Natchitoches Parish, \$144,755.44 was expended on I-49. In Rapides Parish, \$109,414.17 was expended on LA 28, U.S. 71, U.S. 165, U.S. 167, and I-49. In total, \$290,777.50 has been expended on additional mowing and litter pickup cycles.

Pavement Striping/Raised Pavement Marker Application Projects

District 08 continued using supplemental funds on pavement striping/raised pavement marker improvement projects across the district in November. In-house crews completed projects in Vernon and Winn parishes. In Vernon Parish, 2,000 pounds of material and 400 raised pavement markers were placed on LA 117, completing an estimated 6.98 line miles of roadway. Unit 771 placed 1,200 raised pavement markers on

LA 1231-1 and LA 1231-2 in Winn Parish. Additionally, in Winn Parish, crews striped an estimated 40.79 line miles of roadway on LA 34, LA 124, LA 1235, and U.S. 167 using 16,000 pounds of materials and 1,000 gallons of paint. Pavement striping and raised pavement marker application projects have expended \$29,312.00 in November.

Herbicide Application

District 08 is using supplemental funds for herbicide application throughout the district. In November, in-house crews completed projects in Vernon Parish. In November, in-house crews expended \$1,650.00 in materials and applied 30 gallons of herbicide to an estimated 330 acres throughout the district. In Vernon Parish, in-house crews applied herbicide to LA 8, LA 10, LA 121, LA 463, and LA 489.

Sign Repair / Replacement

In an effort to maintain roadway safety, District 08 purchased signs/sign posts using supplemental funds to place new signs or repair/replace signs that have been damaged or are missing. In November, in-house crews replaced 11 damaged signs on LA 623 in Rapides Parish. Additionally, two signs that were damaged due to a vehicle accident were replaced on LA 362 in Avoyelles Parish. Sign repair/replacement projects have expended \$488.02 in November.

Fast Facts

- In-house patch, mill, and overlay projects have used an estimated 311.36 tons of hot mix in November at a cost of \$32,006.22.
- Pavement striping/raised pavement marker application projects have placed an estimated 18,000 pounds of materials, 1,000.00 gallons of paint, and 16,000 pavement markers on the roadway in November.


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$933,765.91
- **Contracts:** \$601,820.91
- **Equipment/rentals:** \$0.00

DOTD District 08

Avoyelles
Grant
Natchitoches
Rapides
Sabine
Vernon
Winn

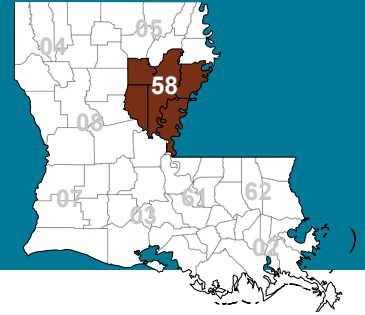

U.S. 425 in 2024



Same location of U.S. 425 in December 2025

Overview

District 58's Unit 711 completed a project to mill out and repave the right lane of a portion of U.S. 425 to correct wheel rutting and rough ride quality. Materials for this project were purchased using this year's supplemental funds totaling \$40,099.18. The total project cost of this project was \$83,207.77.

Herbicides

There were no new herbicide applications during November.

Microsurfacing

The assembly period for this project on U.S. 84 ended in November, but the weather was too wet to begin work on the road during the remainder of the month.

Striping Miles in November

Striping continued with paint supplies from current supplemental funds and the supplemental funds from FY 2025.

- **Tensas Parish:** 18.16 miles on U.S. 65
- **LaSalle Parish:** 10.71 miles on LA 459
- **Catahoula Parish:** 1.38 miles on U.S. 425
- **Agile Work Order Cost:** \$20,852.57
- **Supplemental Funds Cost:** \$3,009.00
- **Supplemental Funds FY25 Cost:** \$10,776.46

Future Projects

- Microsurfacing on five miles of LA 130
- Joint rehabilitation on U.S. 65
- Districtwide tree removal
- Signal upgrade on U.S. 425
- Asphalt overlay
 - U.S. 84 in Concordia
 - LA 124 in Catahoula
 - U.S. 165 in LaSalle
 - LA 4 in Franklin
 - LA 133 in Caldwell
 - Multiple routes in Tensas


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$231,007.30
- **Contracts:** \$31,933.70
- **Equipment/rentals:** \$13,799.12

**DOTD
District 58**

Caldwell
Catahoula
Concordia
Franklin
LaSalle
Tensas

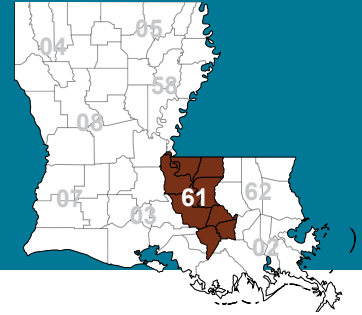

Damaged guardrail



New asphalt

Guardrail Repair

In November, repairs were made on routes with damaged guard rail across the district:

- LA 3251 in Ascension
- U.S. 61 in East Baton Rouge
- LA 10 and U.S. 61 in East Feliciana
- Several locations along U.S. 190 in Pointe Coupee
- I-10 eastbound in St. James Parish

Asphalt and Patching

District paving crews have been on the move this past month. Almost 17 tons of asphalt were laid in Pointe Coupee Parish on U.S. 190 and LA 420. 1,998 tons of asphalt were used on U.S. 190 in West Baton Rouge Parish.

Upcoming Projects

- Tree removal along LA 409 in East Baton Rouge Parish
- Clearing and grubbing along U.S. 190 in East Baton Rouge Parish
- Drainage structure replacement in Ascension, East and West Baton Rouge, and East Feliciana parishes
- Ditch/pipe/box culvert cleaning in East and West Baton Rouge parishes
- Geo-lined pipe on LA 67 in East Feliciana Parish


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$901,321.00
- **Contracts:** \$502,468.00
- **Equipment/rentals:** \$0.00

DOTD District 61

Ascension
Assumption
East/West Baton Rouge
East/West Feliciana
Iberville
Pointe Coupee
St. James

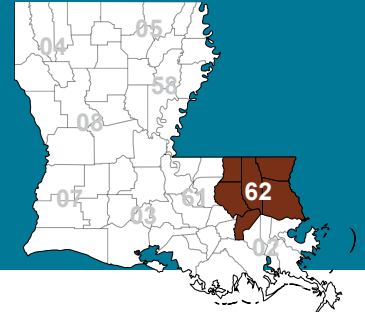

Installation of radar detection equipment



New pavement striping

Asphalt Overlay

Unit 550 used 1,242 tons of asphalt to finish the overlay project on LA 442 in Tangipahoa Parish, totaling \$99,323.

Guardrail Repair

In November, \$39,423 was spent on the guardrail repair contract at the following 11 locations within the district:

- LA 1036 by Montpelier in St. Helena
- I-10 in St. John

- Five spots on I-55 in Tangipahoa
- I-12 and LA 1036 in Livingston
- Two spots on I-12 in St. Tammany

Radar Detection

Traffic signal electricians installed radar detection equipment at U.S. 190B (West 21st Avenue) at LA 21 (Tyler Street) in Covington in St. Tammany Parish, and also at the intersection of U.S. 190 (West Thomas Street) and North Linden Street in Hammond in Tangipahoa Parish.

Roadway Striping

Fresh pavement striping was applied to LA 442 in Tangipahoa Parish, LA 21 and LA 38 in Washington Parish, and LA 22 over the Tickfaw River bridge near Killian in Livingston Parish.

Upcoming Projects

- Box culvert, cross drain, and ditch cleaning throughout District 62
- I-10 crack sealing
- Asphalt patching and overlays along several routes throughout the district
- Tree removal along the interstate right-of-way
- Scrub seals on LA 10, LA 60, and LA 43

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$453,612.00
- **Contracts:** \$451,965.00
- **Equipment/rentals:** \$0.00

DOTD District 62

Livingston
St. Helena
St. John the Baptist
St. Tammany
Tangipahoa
Washington
