


Louisiana Transportation Infrastructure Fund

February 2026



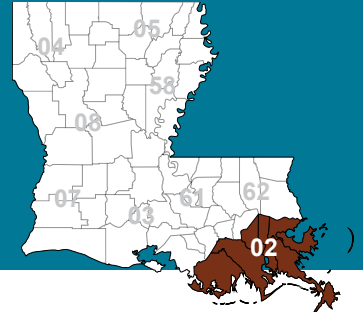

Repaired bridge rail on I-10 in St. Charles Parish



Concrete poured on LA 18 in Jefferson Parish

I-10 Westbound Bridge Rail Repair

A 15-linear-foot section of damaged concrete bridge rail was removed and replaced on I-10 westbound near mile marker 214.5 in St. Charles Parish. Total cost for the bridge rail replacement was \$36,150.00 and was completed by Buck Town Contractors & Co.

LA 18/18S Asphalt Patching and Overlay

Kelly Industries returned on site to finish contract items at the intersection of LA 18 and the Westbank Expressway. Work on a new concrete lid for a catch basin, removal and replacement of a pedestrian ramp, and new curb and gutter concrete work were completed in early February. All contract items are now finished for this project, which is awaiting final acceptance. To date, \$834,145.93 has been paid out on this project. The total estimated cost of this project is \$933,410.85.

DOTD District 02

Jefferson
Lafourche
Orleans
Plaquemines
St. Bernard
St. Charles
Terrebonne


Ongoing and Upcoming Work

- The notice-to-proceed was issued on February 9, 2026, for LA 428 pavement patching in Orleans Parish. Work on this project, as well as LA 308 pavement patching in Lafourche Parish, is slated to begin next month.
- The U.S. 61 pavement patching project in St. Charles Parish is still ongoing.
- District 02 has paid a total of \$120,270.39 on contract guardrail repairs since the start of the fiscal year.

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$0.00
- **Contracts:** \$1,892,371.19
- **Equipment/rentals:** \$0.00

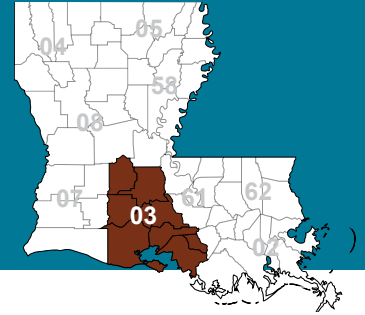

Crews installing a temporary steel plate in Acadia Parish

Contracts

- \$17,653.17 was paid toward the District 03 guardrail repair contract this month for the repair of guardrail located on LA 115 in Evangeline Parish, I-49 in St. Landry Parish, LA 13 in Acadia Parish, U.S. 90 in St. Mary Parish, and LA 723 and I-49 in Lafayette Parish.
- The three new maintenance sweeping contracts began cycles:
 - I-10 median concrete barrier wall (single cycle): \$22,671.00
 - I-10 from I-49 across the Basin Bridge to Ramah (additional cycles through end of FY 26, including median concrete barrier): \$14,950.53
 - U.S. 90 Morgan City Bridge (St. Mary Parish): \$39,388.00
- The \$429,110.00 bridge approach slab undersealing repair project, designating structures in Acadia, Lafayette, and St. Martin parishes, began this month in Acadia Parish.
- The \$511,939.99 contract to repair 254 linear feet of concrete barrier across 25 designated locations in Acadia, St. Martin, and St. Landry parishes started in early February and is expected to be complete by the end of March.

Materials

- Funds for repairing roadway shrinkage, cracking, and pavement faulting:
 - \$32,014.00 (327 tons of asphalt) allocated for continued work on LA 82 in Vermilion Parish

DOTD District 03

Acadia
Evangeline
Iberia
Lafayette
St. Landry
St. Martin
St. Mary
Vermilion

- \$4,320.00 (43 tons of asphalt) allocated for work on LA 70 and LA 182 in St. Mary Parish
- \$18,208.00 (182 tons of asphalt) allocated for work on U.S. 90 in Iberia Parish
- \$20,548.00 (194 tons of asphalt) allocated for work performed on LA 103 in St. Landry Parish
- \$47,139.00 spent in support of LA 682 overlay project work.
- \$21,601.00 spent on a pipe for a culvert replacement on LA 35 in Acadia Parish.
- \$2,135.00 allocated for spare parts and materials for bridge repairs.
- The purchase of \$444,540.00 in striping materials for districtwide striping applications (to be completed this fiscal year) has been finalized, along with the purchase of raised pavement markers for \$20,492.00.
- A 4x4x1 steel plate purchased in September was used during a late afternoon emergency call-out when an area on a major boulevard in Acadia Parish collapsed, creating a hole in the center of a travel lane. The local maintenance crew went to the site with hot mix and met personnel from District 03 headquarters, who transported one of the steel plates to cover the hole as a temporary patch, preventing an extended road closure until repair can be completed.
- Installation of the moveable bridge sewer treatment plants purchased last month, work that was previously outsourced, was completed by District 03 maintenance crews at the Adeline Canal Bridge in St. Mary Parish and the Humble Canal bridges in Vermilion Parish.


Equipment

- Finalized the purchase and awaiting transport from headquarters of a force feed loader for District 03 for \$323,430.88.
- Monthly equipment rental cost of \$293,590.48 for dump trucks, bucket trucks, rollers, sweepers, etc.

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$1,186,775.80
- **Contracts:** \$1,413,679.77
- **Equipment/rentals:** \$920,307.14

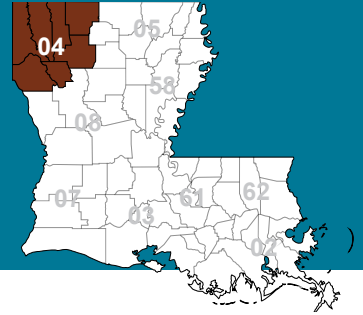

Area of LA 511 needing repairs in Caddo Parish

Contractors will be removing deteriorated areas and pouring new concrete in its place.

The cost of the project is approximately \$692,698.

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$3,077,317.86
- **Contracts:** \$692,698.00
- **Equipment/rentals:** \$34,918.40

DOTD District 04

Bienville
Bossier
Caddo
Claiborne
DeSoto
Red River
Webster




Contractors drilling tie bars for the concrete pour

Roadway Improvements: Roadway Repairs

LA 511 (West 70th Street) Concrete Project

On Monday, February 23, the LA 511 (West 70th Street) project in Caddo Parish officially started. Approximately 0.9 miles of the Shreveport section of the highway between Jewella Avenue and U.S. 171 (Hearne Avenue) will be seeing some much-needed repairs to the concrete travel lanes.

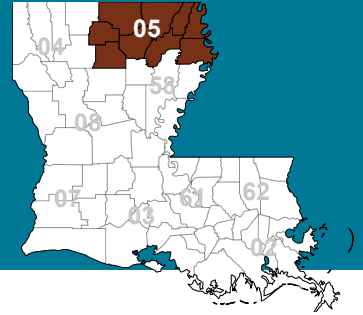

New girders installed on the bridge on LA 550 in Union Parish



Radar installation on a signal along U.S. 80

Bridge Repair Necessary on LA 550 in Union Parish

On LA 550 in Union Parish, a bridge was closed for necessary repairs. Inspection of this bridge showed two timber girders on span 2 that were severely cracked and needed to be replaced. Two 6"x16"x20" timber girders were added to girders 12 and 13 to reinforce the bridge. Brackets were also needed and were fabricated to hold the girders in place. The amount spent for the two girders totaled \$1,102.74.

Installation of Districtwide Radar Detection Equipment

The districtwide signal crew continues with the installation of new radar detection equipment purchased with supplemental funds. In February, the signal crew installed radar detection at three intersections: two signals on U.S. 80 and one signal on U.S. 165 in Ouachita Parish. Material costs for all three projects were \$48,915.00.

Asphalt Projects Begin with Warmer Weather

A hot mix overlay project began on 0.42 miles of LA 134 in West Carroll Parish. 161.94 tons of hot mix were used at a cost of \$18,218.25. Crews in East Carroll Parish completed a full depth patching on LA 134. This project required digging out the base failure and replacing it with 15.12 tons of new asphalt material at a cost of \$1,701.00.


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$688,009.64
- **Contracts:** \$149,520.44
- **Equipment/rentals:** \$338,987.00

DOTD District 05

East/West Carroll
Jackson
Lincoln
Madison
Morehouse
Ouachita
Richland
Union

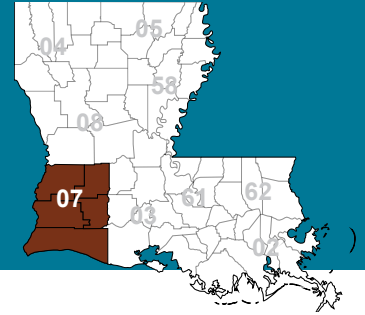

Asphalt leveling on U.S. 171 in Beauregard Parish

Bridge Approach Maintenance

This month, the north approach to a bridge on LA 101 near Hayes was milled and overlaid by our district asphalt crew. 54.01 tons of hot mix asphalt were used for this project. Supplemental-funded materials cost \$6,049.

Maintenance Materials

In February, the District 07 sign crew repaired 324 signs and 689 sign posts throughout our district's five-parish area. Total supplemental funds used for these materials were \$20,883.

The Calcasieu maintenance unit has been full-depth patching on LA 1133 near Carlyss. In February, 62.43 tons of hot mix asphalt were used at a total cost of \$6,992. This patching work continues into March.

The districtwide asphalt crew worked on asphalt leveling on U.S. 171 in Beauregard Parish. 24 tons of hot mix asphalt were used at a total cost of \$2,688.

The District 07 striping crew restriped multiple crosswalks located on state routes around McNeese State University in Lake Charles. 1,500 pounds of white thermoplastic, 132 raised pavement markers, and 200 pounds of glass striping beads were applied to the road. The striping crew also applied thermoplastic material to the parking area at the Toomey rest area near Vinton.

Progress on LA 397 Ditch and Pipe Cleaning Project

Work began on the LA 397 ditch and pipe cleaning project in Calcasieu Parish. This project consists of the cleaning of 37,326 linear feet of ditch and 2,798 linear feet of pipe. Work is anticipated to last two months. Traffic Commander was awarded the project for \$362,140.

Contracted Guardrail Repair

Fourteen guardrail locations were repaired this month: two in Beauregard, nine in Jefferson Davis, and three in Calcasieu. Routes where repairs were made include LA 26, LA 101, LA 102, LA 382, LA 389, LA 1126, LA 1147, and I-10. Supplemental funds cost: \$59,601.

Traffic Signal Improvements

Signal radar upgrades continue. District 07 signal crews upgraded radar detection on signals at two intersections in Calcasieu Parish and two intersections in Jefferson Davis Parish. Materials cost for this detection upgrade: \$119,960.

The signal heads at one intersection in Calcasieu Parish were replaced with polycarbonate material. This lighter material will increase vertical clearance at the intersection. Materials cost: \$3,930.

Milling Contract

A contract to mill approximately 0.97 miles of LA 27 north of Sulphur was awarded to Prairie Contractors this month. This area will be milled by the contractor, and district in-house forces will follow with hot mix asphalt overlay. Bid: \$133,427.32.


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$1,165,151.42
- **Contracts:** \$791,445.93
- **Equipment/rentals:** \$277,309.00

DOTD District 07

Allen
Beauregard
Calcasieu
Cameron
Jefferson Davis

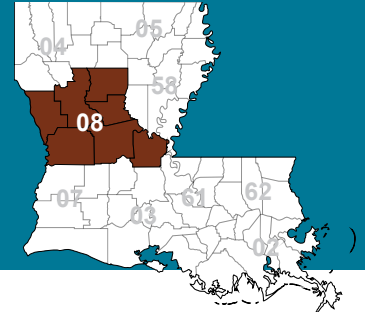

Crews cutting trees using the articulating boom manlift

Patch, Mill, and Overlay Projects

In February, in-house crews milled and overlaid a section of LA 1 and a section of LA 121 in Rapides Parish with 1,502.50 tons of hot mix asphalt at a cost of \$154,757.50. In Sabine Parish, in-house crews continued full-depth patching base failures on LA 476. Crews laid 50.19 tons of hot mix asphalt at a cost of \$5,119.38. This project is complete.

Tree Cutting

District 08 rented a 125-foot articulating boom manlift to be used in Vernon and Sabine parishes for in-house crews to cut trees posing a safety hazard.

Cable Barrier and Guardrail Repair

Supplemental funds are being used to repair damaged cable barrier and guardrail throughout the district in order to ensure roadway safety. In February, two sections of cable barrier in Natchitoches Parish and one section of cable barrier in Rapides Parish were repaired by in-house crews at a cost of \$1,316.97.

Pavement Striping/Raised Pavement Marker Application Projects

District 08 continued using supplemental funds on pavement striping/raised pavement marker improvement projects across the district in February. In-house crews completed projects in Avoyelles, Rapides, Vernon

and Winn parishes. In Avoyelles Parish, Unit 771 placed 800 raised pavement markers on LA 114. In Rapides and Vernon parishes, an estimated 918 linear feet of roadway were striped on LA 28 and LA 392 using hot tape. Additionally, in Vernon Parish, in-house crews striped 5.30 lane miles on LA 392 and placed 2,800 raised pavement markers on LA 8. In Winn Parish, in-house crews striped approximately 63.70 lane miles on LA 34, LA 472, and U.S. 84. Also in Winn Parish, Unit 771 placed 1,400 raised pavement markers on LA 1236. Pavement striping and raised pavement marker application projects cost \$36,792.07 in February.

DOTD District 08

Avoyelles
Grant
Natchitoches
Rapides
Sabine
Vernon
Winn

Sign Repair/Replacement

In February, in-house crews replaced/repairs 413 damaged signs/posts throughout the district in an effort to maintain roadway safety on LA 1, LA 6, LA 8, LA 28, LA 29, LA 34, LA 107, LA 114, LA 121, LA 123, LA 126, LA 184, LA 454, LA 487, LA 488, LA 492, LA 494, LA 1187, LA 1217, LA 1226, LA 1239-1, LA 1243, LA 3144, U.S. 71, U.S. 165, U.S. 167, and U.S. 171. Sign repair/replacement projects cost \$8,769.02.


Fast Facts

- District 08 spent \$861.00 to rent a scissor lift. The scissor lift will be used to construct the bulk salt storage that was purchased with LTIF funds.
- District 08 purchased an off-road asphalt distributor and two skid steer loaders at a cost of \$236,266.34 in LTIF funds.

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$1,742,356.47
- **Contracts:** \$1,921,224.01
- **Equipment/rentals:** \$246,746.34

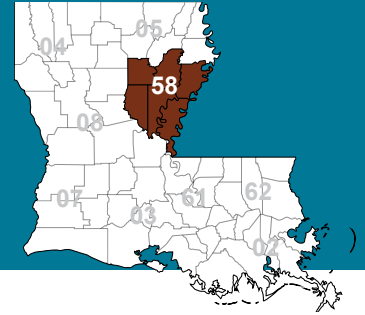

Unit 710 operating the debris truck on LA 4

Updates

District 58 rented four debris trucks to assist with winter storm Fern clean-up. The rental on two of these trucks was extended for continued right-of-way cleanup projects. The cost of the total truck rental was \$42,000.00.

District 58 awarded its microsurfacing project for LA 130 in Franklin Parish to Vance Brothers, Inc. for \$432,864.73.

The new microsurfacing contract for U.S. 84 in LaSalle Parish was awarded to Intermountain Slurry Seal, Inc. for \$565,567.25. This project will address the section of U.S. 84 from LA 772 in Midway to LA 459 in Jena.

The PCCP patching project on U.S. 65 in Tensas Parish was awarded to Bentz Construction Group, LLC for \$462,762.00.

Tree Removal

The tree removal contract in LaSalle, Catahoula, and Concordia awarded to Traffic Commander, LLC is in the assembly period. The contract for Franklin, Caldwell, and Tensas awarded to Alison Enterprises is also in the assembly period.

Microsurfacing

The project on U.S. 84 in Catahoula Parish has been winterized and will begin in spring when the weather allows. Vance Brothers also has received their first payment of \$7,500.00.

Herbicides

Herbicide application will begin again in March.

Future Projects

- Joint rehabilitation on U.S. 65
- Signal upgrade on U.S. 425 in Franklin Parish
- Asphalt overlay:
 - U.S. 84 in Concordia
 - LA 124 in Catahoula
 - U.S. 165 in LaSalle
 - LA 4 in Franklin
 - LA 133 in Caldwell
 - LA 605 in Tensas

Striping Miles in February

Franklin Parish: 16.7 miles on LA 135 and LA 130

- Agile work order cost: \$18,538.34
- Supplemental funds cost: \$4,047.40
- Supplemental funds FY 25 cost: \$9,807.63


Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$235,054.70
- **Contracts:** \$40,708.75
- **Equipment/rentals:** \$133,502.87

**DOTD
District 58**

Caldwell
Catahoula
Concordia
Franklin
LaSalle
Tensas

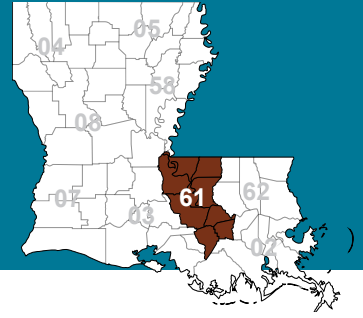

New pipe on LA 42 in Ascension Parish



Guardrail repair before and after

Pipe Installation

To date, 240 feet of pipe have been installed on LA 42 in Ascension Parish, along with 144 cubic yards of hot mix.

Guardrail Repair

Repairs were made on guardrails on LA 308 and I-10 west in Ascension Parish. Five repairs were made in East Baton Rouge Parish on I-110 and I-12. One guardrail was repaired on LA 19 in East Feliciana Parish. Three repairs were made in Pointe Coupee Parish on LA 1 and U.S. 190.

Upcoming Projects

- Tree removal along LA 409 in East Baton Rouge Parish
- Clearing and grubbing along U.S. 190 in East Baton Rouge Parish
- Drainage structure replacement in East Baton Rouge, West Baton Rouge, and East Feliciana parishes
- Ditch/pipe/box culvert cleaning in East Baton Rouge and West Baton Rouge parishes
- Geo-lined pipe on LA 67 in East Feliciana Parish


DOTD District 61

Ascension
Assumption
East/West Baton Rouge
East/West Feliciana
Iberville
Pointe Coupee
St. James

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$ 1,744,228.89
- **Contracts:** \$1,346,552.20
- **Equipment/rentals:** \$0.00

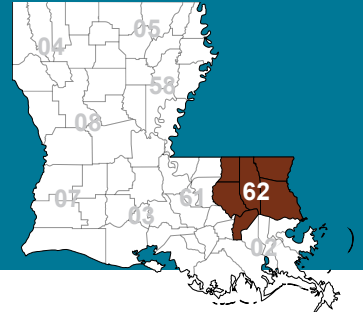

New striping in Livingston Parish



Radar detection equipment installation in St. Tammany Parish

Radar Detection

Radar detection equipment was installed at the U.S. 190/LA 25 intersection in St. Tammany Parish, along with the intersection at LA 22/U.S. 190 frontage road.

Roadway Striping

The yellow and white lines were refreshed on LA 1026 and LA 1064 in Livingston Parish, LA 10 in St. Helena Parish, and LA 435 in St. Tammany Parish from Talisheek Road to LA 41.

Guardrail Repair

Guardrail was repaired in Livingston Parish on LA 16, LA 1024, and LA 441. In St. Helena Parish, there was one repair made on LA 440. In St. Tammany Parish, repairs were made on I-12, LA 435, U.S. 11, and U.S. 190. In Tangipahoa Parish, repairs were made to guardrail on LA 22, LA 38, LA 443, LA 1054, and I-12.

Upcoming Projects

- Box culvert, cross drain, and ditch cleaning throughout the district
- I-10 crack sealing
- Asphalt patching and overlays along several routes
- Tree removal along the interstate right-of-way
- Scrub seals on LA 10, LA 60, and LA 43

Spending

Spending Category and Amount Spent Since July 1, 2025

- **Materials:** \$783,061.39
- **Contracts:** \$545,076.06
- **Equipment/rentals:** \$11,667.00

DOTD District 62

Livingston
St. Helena
St. John the Baptist
St. Tammany
Tangipahoa
Washington
