

LA 352 DRAINAGE IMPROVEMENTS



US 90: RR JET - PINHOOK, LA - LA 88



# REQUEST FOR QUALIFICATIONS

ENTITY CONTRACT NO 4400031036  
STATE PROJECT NO. H.015120.6  
FEDERAL AID PROJECT NO. H015120  
ROOSEVELT BLVD: W NAPOLEON - W METAIRIE (CE&I)  
JEFFERSON PARISH



IN ASSOCIATION WITH:



MICHAEL BAKER INTERNATIONAL

FEBRUARY 4, 2025

LINFIELD, HUNTER & JUNIUS, INC.

25M-010





**LINFIELD, HUNTER & JUNIUS, INC.**

PROFESSIONAL ENGINEERS,  
ARCHITECTS AND SURVEYORS

3608 18<sup>th</sup> Street / Suite 200  
Metairie, Louisiana 70002  
(504) 833-5300 / (504) 833-5350 fax  
LHJ@LHJunius.com

Ralph W. Junius, Jr., P.E.  
Nathan J. Junius, P.E., P.L.S.  
Anthony F. Goodgion, P.E.  
Nathan D. Hills, AIA  
Charles T. Knight, P.E.  
Robert E. Nockton, P.E.  
Mark K. Annino  
Casey M. Genovese, P.E.

Daniel A. Flores, P.E.  
John M. Jackson, P.E.  
Timothy J. Roth, P.E.  
Vincent J. Leco, III, P.E.  
Eric R. Wright, P.E.  
Luis F. Sosa, P.E.  
Richard A. Van Wootten, P.E.

February 4, 2025

Department of Transportation and Development  
1201 Capitol Access Road  
Baton Rouge, LA 70802-4438

**RE: Statement of Qualifications  
Roosevelt Blvd: W Napoleon – W Metairie (CE&I)  
Contract No. 4400031036  
State Project No. H.015120.6  
F.A.P. No. H015120  
Jefferson Parish  
Our File #: 25M-010**

Linfield, Hunter & Junius, Inc. (LH&J) is pleased to submit its Statement of Qualifications on the St. Brenard Pedestrian Improvements (CE&I) project for Louisiana Department of Transportation and Development.

Linfield, Hunter & Junius, Inc. (LH&J) and Michael Baker International, Inc. (MBI) will provide Construction Engineering and Inspections (CE&I) Services for the project.

Contact Information:

Nathan J. Junius, P.E., P.L.S. PTOE, President  
Linfield, Hunter & Junius, Inc., 3608 18<sup>th</sup> Street, Suite 200, Metairie, LA 70002  
[njunius@LHJunius.com](mailto:njunius@LHJunius.com) - 504-833-5300 - 504-833-5350 fax

We look forward to a relationship with Louisiana Department of Transportation and Development.

Very truly yours,

LINFIELD, HUNTER & JUNIUS, INC.

Nathan J. Junius, P.E., P.L.S.  
President

NJJ/dlm  
Enclosures

# DOTD FORM: 24-102

(Revised December 12, 2024)

## PROPOSAL TO PROVIDE CONSULTANT SERVICES

Prime consultant shall complete the DOTD Form 24-102 without altering the Form's text; however, the instruction and/or guidance for Sections 12 through 23 can be removed but do not remove Section title and number.

ANY CONSULTANT FAILING TO SUBMIT ANY OF THE INFORMATION REQUIRED ON THE DOTD FORM 24-102, OR PROVIDING INACCURATE INFORMATION ON THE DOTD FORM 24-102, MAY BE CONSIDERED NON-RESPONSIVE.

|   |   |
|---|---|
| 1. Contract Name as shown in the advertisement  | ROOSEVELT BLVD: W NAPOLEON – W METGAIRIE (CE&I)<br>JEFFERSON PARISH                 |
| 2. Contract Number(s) as shown in the advertisement   | 4400031036  |
| 3. State Project Number(s), if shown in the advertisement   | H.015120.6  |
| 4. Prime consultant name (name must match <u>exactly</u> as registered with the Louisiana Secretary of State where such registration is required by law; including punctuation; <i>include screenshot from SOS at the end of Section 20</i> ) | LINFIELD, HUNTER & JUNIUS, INC.   |
| 5. Prime consultant license number (as registered with the Louisiana Professional Engineering and Land Surveying Board (LAPELS) if registration is required under Louisiana law)  | ENGINEERING – EF.0000510<br>SURVEYING – VF.0000532                                  |
| 6. Prime consultant mailing address   | 3608 18 <sup>TH</sup> STREET, SUITE 200<br>METAIRIE, LA 70002                       |
| 7. Prime consultant physical address (existing or to be established, if location is used as an evaluation criteria)   | 3608 18 <sup>TH</sup> STREET, SUITE 200<br>METAIRIE, LA 70002                       |
| 8. Name, title, phone number, and email address of prime consultant's contract point of contact   | NATHAN J. JUNIUS, P.E., P.L.S.<br>PRESIDENT<br>504-833-5300<br>NJUNIUS@LHJUNIUS.COM |
| 9. Name, title, phone number, and email address of the official with signing authority for this proposal  | NATHAN J. JUNIUS, P.E., P.L.S.<br>PRESIDENT<br>504-833-5300<br>NJUNIUS@LHJUNIUS.COM |

Prime consultant should enter the firm name in the footer at the bottom of this page. (It will carry over to subsequent pages.)

**10.** This is to certify that all information contained herein is accurate and true, and that the team presently has sufficient staff to perform these services within the designated time frame. By submitting this proposal, proposer certifies that it is not engaged in a boycott of Israel and it will, for the duration of its contract obligations, refrain from a boycott of Israel. Proposer also certifies and agrees that the following information is correct: In preparing its response, the proposer has considered all proposals submitted from qualified, potential subcontractors and suppliers, and has not, in the solicitation, selection, or commercial treatment of any subcontractor or supplier, refused to transact or terminated business activities, or taken other actions intended to limit commercial relations, with a person or entity that is engaging in commercial transactions in Israel or Israeli-controlled territories, with the specific intent to accomplish a boycott or divestment of Israel. The proposer also has not retaliated against any person or other entity for reporting such refusal, termination, or commercially limiting actions. DOTD reserves the right to reject the response of the bidder or proposer if this certification is subsequently determined to be false, and to terminate any contract awarded based on such a false response.



Signature above shall be the same person listed in Section 9:

February 4, 2025

Date:

**Pursuant to Act No. 581 of the 2024 Louisiana Legislature Regular Session, proposer further certifies that it does not have a practice, policy, guidance, or directive that discriminates against a firearm entity or firearm trade association based solely on the entity's or association's status as a firearm entity or firearm trade association. In addition, proposer certifies it will not discriminate against a firearm entity or firearm trade association during the term of the contract based solely on the entity's or association's status as a firearm entity or firearm trade association.**

**11.** If a Disadvantaged Business Enterprise (DBE) goal has been set for this advertisement, indicate which firm(s) will be used to meet the DBE goal and each firm(s)' percentage.

Firm(s):

N/A



Firm(s)' %:



**12. Discipline Table:**

As indicated in the advertisement, insert a completed table here. The percentages for the prime and sub-consultants must total 100% for each discipline, as well as the overall total percent of the contract.

The **only** disciplines to be used are listed in the drop down in each row (Appraiser, Bridge, CE&I/OV, CPM, Data Collection, Environmental, Geotech, ITS, Other (must specify), Planning, Right-of-Way, Road, Survey, and Traffic). **Remove rows as needed.**

| Discipline(s)       | % of Overall Contract | <br>Linfield, Hunter & Junius, Inc.<br>(Prime) | <br>Michael Baker International, Inc.<br>(Subconsultant) | Each Discipline must total to 100% |
|---------------------|-----------------------|---|---|------------------------------------|
| CE&I/OV             | 100%                  | 85%   | 15%   | <b>100%</b>                        |
| Percent of Contract | <b>100%</b>           | 85%   | 15%   |                                    |

**13. Firm Size:**


For all firms that are part of this team, indicate the approximate number of personnel to be committed to this contract, by DOTD Job Classification and the total number of personnel within the firm that could provide support, if needed. If a specialized job classification is required and not included on the DOTD job classification list, specify “Other (must specify)” and include the classification title inside the parentheses.

The DOTD Job Classification(s) to be used can be found at the following link:

[http://wwwsp.dotd.la.gov/Inside\\_LaDOTD/Divisions/Engineering/CCS/Job\\_Qualification/Job%20Classifications%20with%20Descriptions.pdf](http://wwwsp.dotd.la.gov/Inside_LaDOTD/Divisions/Engineering/CCS/Job_Qualification/Job%20Classifications%20with%20Descriptions.pdf)

| Firm name                         | DOTD Job Classification | Number of personnel committed to this contract | Total number of personnel available in this DOTD Job Classification (if needed) |
|-----------------------------------|-------------------------|--|---|
| Linfield, Hunter & Junius, Inc.   | Principal               | 1  | 1   |
|                                   | Supervisor - Eng        | 1  | 2   |
|                                   | Engineer                | 1  | 3   |
|                                   | Inspector - Certified   | 1  | 1   |
| Michael Baker International, Inc. | Inspector - Certified   | 1  | 4   |

**14. Organizational Chart:**

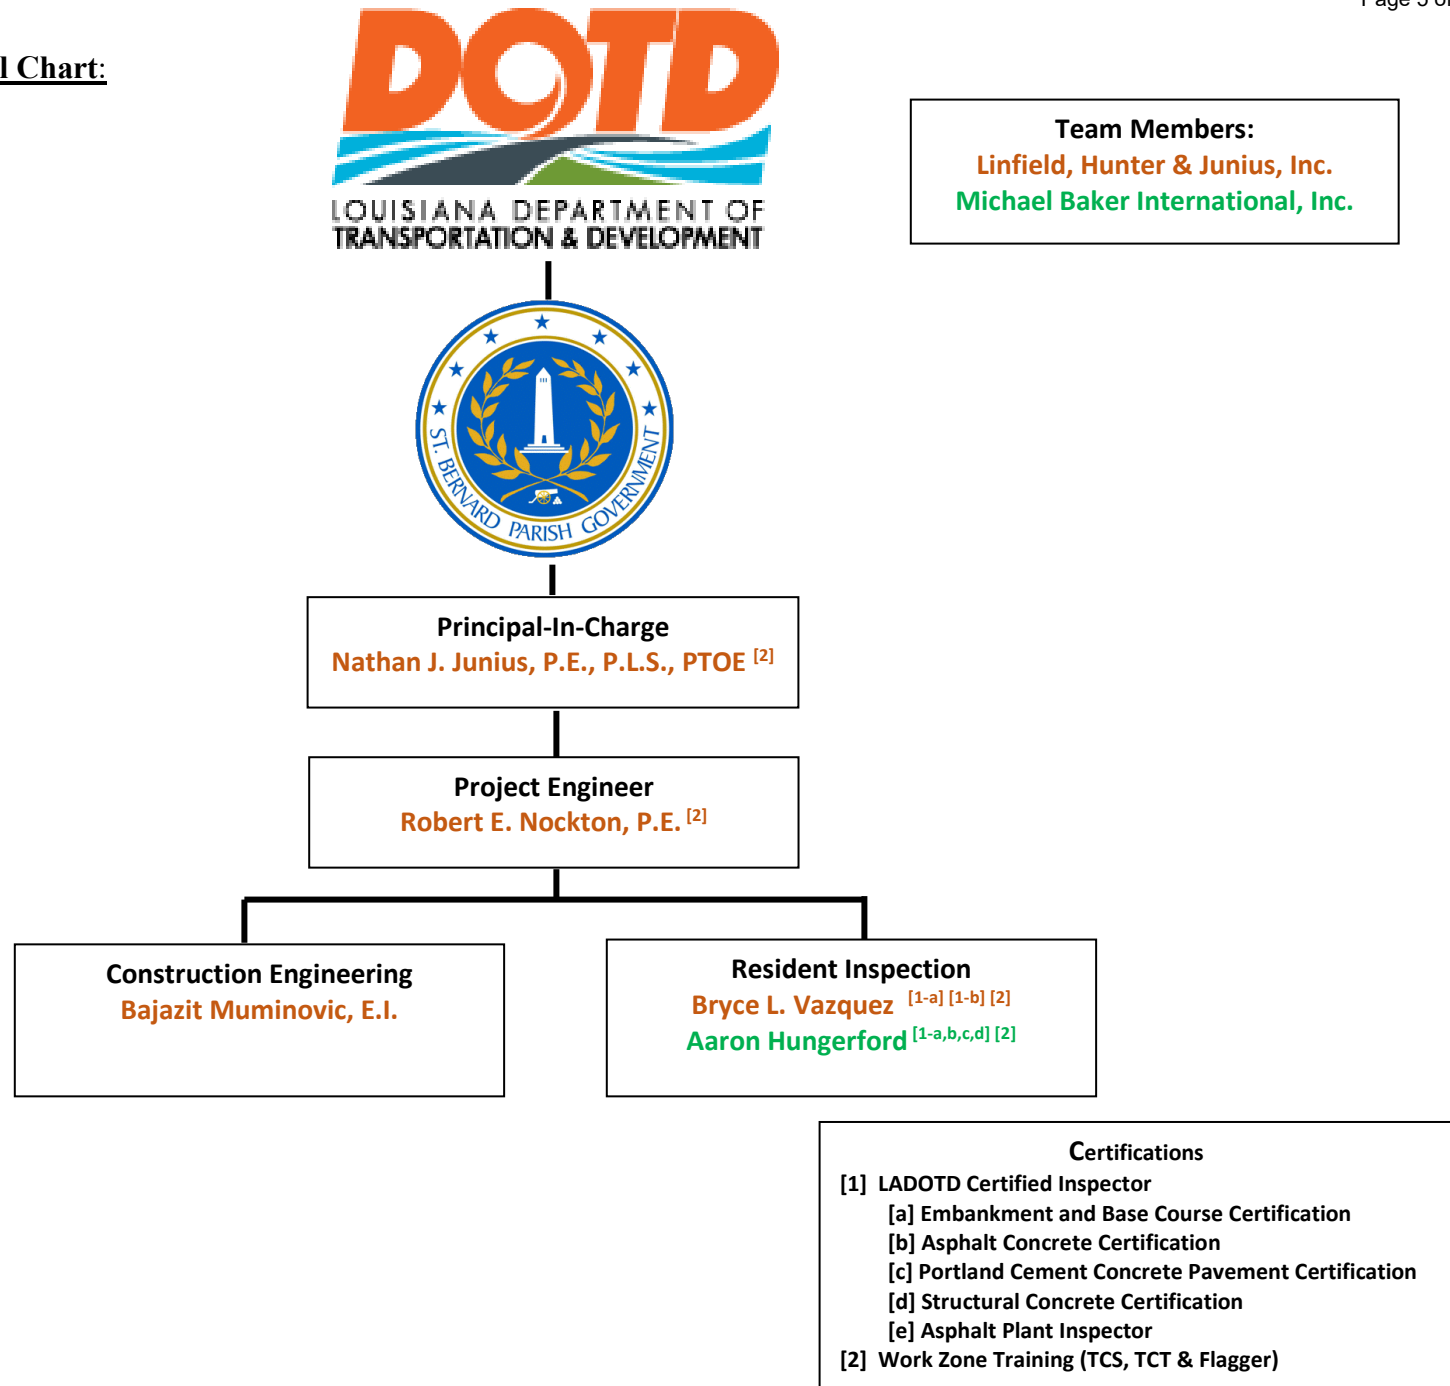




**15. Minimum Personnel Requirements:**

| MPR No.<br>Do not insert<br>wording<br>from ad | Personnel being used to meet the MPR<br>(Individual(s) may not satisfy more than one MPR<br>unless specifically allowed by Attachment B of the<br>advertisement) | Firm employed by                | Type of license and<br>discipline meeting MPR/<br>certification & number<br>(Ex: PE # - Civil) | State<br>of<br>license | License /<br>certification<br>expiration date |
|--|--|---------------------------------|--|------------------------|---|
| 1  | Nathan J. Junius, P.E., P.L.S.   | Linfield, Hunter & Junius, Inc. | PE.0031843-Civil<br>Engineer   | LA                     | Exp. 09/30/2025                               |
| 2  | Nathan J. Junius, P.E., P.L.S.   | Linfield, Hunter & Junius, Inc. | PE.0031843-Civil<br>Engineer   | LA                     | Exp. 09/30/2025                               |
| 3  | Robert E. Nockton, P.E.  | Linfield, Hunter & Junius, Inc. | PE.0028802-Civil<br>Engineer   | LA                     | Exp. 09/30/2026                               |


(Add rows as needed)

**16. Staff Experience:**

|   |   |  |   |
|---|---|--|---|
| Firm employed by – <b>Linfield, Hunter &amp; Junius, Inc.</b>                     |   |  |   |
| Name  | <b>Nathan J. Junius, P.E., P.L.S., P.T.O.E.</b>   |  | Years of experience with this firm/employer |
| Title   | President   |  | 24  |
| Degree(s) / Years / Specialization  |   | Years of experience with other firm(s)/employer(s)   |   |
|   |   | 0  |   |
| Degree(s) / Years / Specialization  |   | Tulane University BS/2001/Civil Engineering<br>University of Texas at Austin MS/2002/Civil Engineering |   |
| Active registration number / state / expiration date                              |   | PE.0031843 / LA / 09/30/2021<br>PLS.0004958 / LA / 09/30/2021  |   |
| Year registered   | 2005<br>2006  | Discipline   | Civil Engineering<br>Land Surveying         |
| Contract role(s) / brief description of responsibilities                          |   | Principal-In-Charge – <b>(Satisfies MPRs 1,2 and 3)</b>  |   |
| Experience dates (mm/yy–mm/yy)  | Experience and qualifications relevant to the proposed contract; <i>i.e.</i> , “designed drainage”, “designed girders”, “designed intersection”, etc.   |  |   |
|  | <p>Junius has over 22 years of project management, engineering design and construction management experience, with specialized expertise in the planning, permitting, design and construction management for a diverse range of public and private sector projects. Civil projects include major drainage canals, drainage pump stations, site developments, miles of streets, wastewater treatment plants, sewage collections systems, sewer force mains and waterline distribution projects. He has also served as an expert in disputes involving drainage and land surveying.</p> <p>Mr. Junius has been Past President of The American Society of Civil Engineers, (ASCE), New Orleans Chapter; Past President, American Public Works Association (APWA), New Orleans Metropolitan Branch; Member, American Society of Military Engineers (SAME); Member, American Council of Engineering Companies; Member, Louisiana Engineering Society; Member, Louisiana Society of Professional Surveyors</p> <p>ATSSA – Traffic Control Technician/Supervisor<br/>ATSSA – Traffic Certified Flagger</p> |  |   |
| 10/2023 – Ongoing   | <p><b><u>DOTD SP H.014415: LA 352 DRAINAGE IMPROVEMENT (CE&amp;I), ST. MARTIN PARISH, LA</u></b></p> <p>Junius is Principal-In-Charge for this project that includes drainage improvements along LA 352 from LA 347 east approximately 1,000 linear feet. Junius oversees and manages all Linfield, Hunter &amp; Junius, Inc. (LH&amp;J) personnel involved with this project.</p>  |  |   |
| 09/2023 – Ongoing   | <p><b><u>DOTD SP H.009629: US 90: RR JCT – PINHOOK, LA 92 – LA 88 (CE&amp;I), IBERIA, LAFAYETTE &amp; ST. MARTIN PARISHES, LA</u></b></p> <p>Junius is Principal-In-Charge for this project that includes replacement of concrete roadway panels, milling and</p>   |  |   |


|                      |  |
|----------------------|--|
|                      | overlaying of asphalt shoulders, slab-jacking of existing concrete roadway panels and pavement striping along US 90/US 167 between the railroad crossing and E. Pinhook Road and along US 90 between LA 92 and LA 88. Junius oversees and manages all Linfield, Hunter & Junius, Inc. (LH&J) personnel involved with this project.   |
| 11/2019 –<br>04/2023 | <b><u>VULCAN STREET DRAINAGE IMPROVEMENTS, JEFFERSON PARISH, LA</u></b><br>Junius was Principal-In-Charge for this project that included drainage improvements along Vulcan Street between Par 3 Drive and Telestar Street including replacement of gravity sewer, replacement of concrete roadway pavement, curbing, driveways and sidewalks. Linfield, Hunter & Junius, Inc. provided the following services for this project: topographic surveying, engineering design and preparation of plans and specifications, coordination with private utilities for relocations, assistance with advertisement and bidding, construction engineering, resident inspection and preparation of as-built drawings. Junius oversaw and managed all personnel involved with this project. |
| 03/2006 –<br>11/2014 | <b><u>JEFFERSON PARISH DISTRICT 5 STREETS PROJECT, METAIRIE, LA</u></b><br>Junius was Project Manager of this project which included design and construction management including resident inspection for the rehabilitation of over 100 flood damaged streets on the East Bank of Jefferson Parish. Linfield, Hunter & Junius, Inc. provided the following services for this project: engineering design and preparation of plans and specifications, assistance with advertisement and bidding, construction engineering and resident inspection. Junius oversaw and supervised all personnel involved with the engineering design, construction engineering and resident inspection of the project.   |
| 08/2005 –<br>10/2007 | <b><u>USACE CONSTRUCTION SUPPORT SERVICES, NEW ORLEANS, LA</u></b><br>Junius was the Project Manager of this project which included design and construction management. In these types of support services, we routinely perform Site Visits, review Contractor Submittals, evaluate Value Engineering Proposals, respond to Unknown Conditions and answer Requests for Information submittals. LH&J had 5 resident inspectors working on this project.  |
| 02/2008 –<br>10/2012 | <b><u>EAST AND WEST LIVINGSTON PLACE ROADWAY IMPROVEMENTS, METAIRIE, LA</u></b><br>Junius was the Project Manager of this project which included design and construction management. This project consisted of the reconstruction of East and West Livingston Place including installation of curb replacement, sidewalk replacement and ADA ramps. Junius oversaw and supervised engineering design, construction engineering and resident inspection and managed the contract for the project.   |



|  |  |   |   |
|--|--|---|---|
| Firm employed by – <b>Linfield, Hunter &amp; Junius, Inc.</b>  |  |   |   |
| Name   | <b>Robert E. Nockton, P.E.</b>   |   | Years of experience with this firm/employer |
| Title  | Vice President   |   | 30  |
|  |  | Years of experience with other firm(s)/employer(s)    | 0   |
| Degree(s) / Years / Specialization   |  | Rice University/BS/Civil Engineering/1995             |   |
| Active registration number / state / expiration date   |  | LA/Civil/PE.0028802                                   |   |
| Year registered  | 2000   | Discipline  | Civil Engineering                           |
| Contract role(s) / brief description of responsibilities   |  | Project Engineer – <b>(Satisfies MPRs 1, 2 and 3)</b> |   |
| Experience dates (mm/yy–mm/yy)   | Experience and qualifications relevant to the proposed contract; <i>i.e.</i> , “designed drainage”, “designed girders”, “designed intersection”, etc.  |   |   |
|  <b>REGISTRATIONS/CERTIFICATIONS:</b><br>Member APWA; Member ASCE<br>ATSSA – Traffic Control Technician/Supervisor<br>ATSSA – Traffic Certified Flagger |  |   |   |
| 10/23 – Ongoing  | <b><u>DOTD SP H.014415: LA 352 DRAINAGE IMPROVEMENT (CE&amp;I), ST. MARTIN PARISH, LA</u></b><br>Nockton is the Project Engineer for this project that includes drainage improvements along LA 352 from LA 347 east approximately 1,000 linear feet. Linfield, Hunter & Junius, Inc. (LH&J) is providing resident inspection for this project. Nockton manages the contract and oversees the inspection of this project.   |   |   |
| 09/23 – Ongoing  | <b><u>DOTD SP H.009629: US 90: RR JCT – PINHOOK, LA 92 – LA 88 (CE&amp;I), IBERIA, LAFAYETTE &amp; ST. MARTIN PARISHES, LA</u></b><br>Nockton is the Project Engineer for this project that includes replacement of concrete roadway panels, milling and overlaying of asphalt shoulders, slab-jacking of existing concrete roadway panels and pavement striping along US 90/US 167 between the railroad crossing and E. Pinhook Road and along US 90 between LA 92 and LA 88. Linfield, Hunter & Junius, Inc. (LH&J) is providing resident inspection for this project. Nockton manages the contract and oversees the inspection of this project. |   |   |
| 11/19 – 04/23  | <b><u>VULCAN STREET DRAINAGE IMPROVEMENTS, JEFFERSON PARISH, LA</u></b><br>Nockton was the Project Engineer for this project that included drainage improvements along Vulcan Street between Par 3 Drive and Telestar Street including replacement of gravity sewer, replacement of concrete roadway pavement, curbing, driveways and sidewalks. Linfield, Hunter & Junius, Inc. provided the following services for this project: topographic surveying, engineering design and preparation of plans and specifications, coordination with private utilities for relocations, assistance with project advertisement and bidding, construction     |   |   |


|                 |   |
|-----------------|---|
|                 | engineering, resident inspection and preparation of as-built drawings. Nockton was in charge of all engineering design, construction engineering, resident inspection and as-built drawing preparation.   |
| 12/20 - Ongoing | <p><b><u>WATER AND SEWERAGE EXTENSION – LINDBERG DRIVE TO EAST I-10 SERVICE ROAD, SLIDELL, LA</u></b></p> <p>Nockton is the Project Engineer for this project that includes the extension of water and sewerage across the I-10 from Lindberg Drive to the East I-10 Service Road. Linfield, Hunter &amp; Junius, Inc. is providing the following services for this project: engineering design and preparation of plans and specifications, assistance with permitting, assistance with project advertisement and bidding, construction engineering and preparation of as-built drawings. Work included obtaining two permits from LADOTD for the crossing of I-10 by directional drilling of water and sewerage pipe. Nockton is in charge of all engineering design, permitting and construction engineering.</p>  |
| 11/12 – 03/19   | <p><b><u>CLUB DELUXE ROAD WIDENING AND ELEVATION, HAMMOND, LA</u></b></p> <p>Nockton was the Project Engineer for this project that included the widening and elevation of Club Deluxe Road between US 51 (South Morrison Road) to Veterans Boulevard, approximately one and one half miles, including the installation of new subsurface drainage along each side of the roadway. The project also included modification to the traffic signal at the US 51/Club Deluxe Road intersection in accordance with LADOTD requirements since US 51 is a state maintained highway. Linfield, Hunter &amp; Junius, Inc. provided the following services for this project: topographic surveying, engineering design and preparation of plans and specifications, assistance with permitting, coordination with private utilities for relocations, assistance with project advertisement and bidding, construction engineering and preparation of as-built drawings. Nockton was in charge of all engineering design, permitting, construction engineering and resident inspection.</p> |
| 07/07 – 06/16   | <p><b><u>ELEVATION AND RECONSTRUCTION OF TIDEWATER ROAD, VENICE, LA</u></b></p> <p>Nockton was the Project Engineer for this project that included the raising of approximately 3 miles of critical roadway serving the Venice Port facilities outside of the hurricane protection levee system. Linfield, Hunter &amp; Junius, Inc. provided the following services for this project: topographic surveying, engineering design and preparation of plans and specifications, assistance with permitting, assistance with project advertisement and bidding, construction engineering, resident inspection and preparation of as-built drawings. Nockton was in charge of all engineering design, permitting, construction engineering and resident inspection.</p>   |

**16. Staff Experience:**

|  |   |  |   |   |
|--|---|--|---|---|
| Firm employed by – <b>Linfield, Hunter &amp; Junius, Inc.</b>  |   |  |   |   |
| Name   | <b>Bajazit Muminovic, E.I.</b>  |  | Years of relevant experience with this employer     | 4 |
| Title  | Civil Engineer Intern   |  | Years of relevant experience with other employer(s) | 0 |
| Degree(s) / Years / Specialization   |   | Louisiana State University/B.S./2021/Civil Engineering |   |   |
| Active registration number / state / expiration date   |   | EI.0035270 / LA / 09/21/2025                           |   |   |
| Year registered  | 2022  | Discipline   | Civil Engineer                                      |   |
| Contract role(s) / brief description of responsibilities   |   | Engineer Intern – Construction Engineering             |   |   |
| Experience dates (mm/yy–mm/yy)   | Experience and qualifications relevant to the proposed contract; i.e., “designed drainage”, “designed girders”, “designed intersection”, etc. Experience dates should cover the time specified in the applicable MPR(s).  |  |   |   |
|  <b>REGISTRATIONS/CERTIFICATIONS:</b> |   |  |   |   |
| 09/23-11/23  | <b><u>DOTD SP H.009629: US 90: RR JCT – PINHOOK, LA 92 – LA 88 (CE&amp;I), IBERIA, LAFAYETTE &amp; ST. MARTIN PARISHES, LA</u></b><br>Muminovic was a Resident Inspector for this project that includes replacement of concrete roadway panels, milling and overlaying of asphalt shoulders, slab-jacking of existing concrete roadway panels and pavement striping along US 90/US 167 between the railroad crossing and E. Pinhook Road and along US 90 between LA 92 and LA 88. Muminovic monitored full-depth concrete patching, repair base failures, dowel bar retrofit, cleaning and resealing, striping and related work, slab jacking of concrete panels, milling of old asphalt shoulder and installation of new asphalt. He also documented daily activity including contractor personnel and equipment, inspected the contractor’s traffic control for proper sign and barricade usage and placement and maintained field records using Ladd’s Site Manager Program/Headlight. |  |   |   |
| 11/23-ongoing  | <b><u>NEW ORLEANS LANDBRIDGE SHORELINE STABILIZATION AND MARSH CREATION PROJECT (CPRA), SLIDELL, LA</u></b><br>Muminovic is Engineer Intern/Resident Inspector for this project that consists of the hydraulic dredging of three marsh creation areas including the construction of earthen containment dikes. Linfield, Hunter & Junius, Inc. is providing construction engineering and resident inspection services for this project. Muminovic reviews contractor production submittals and contractor invoice quantities and prepares change order backup. Muminovic also provides resident inspection on an as-needed basis.   |  |   |   |



|               |   |
|---------------|---|
| 10/22 – 04/23 | <b><u>HOLMES BOULEVARD REHABILITATION, TERRYTOWN, LA</u></b><br>Muminovic was Resident Inspection for this project that consisted of the rehabilitation of Holmes Boulevard from Terry Parkway to Berhman Highway. Muminovic measured dimensions, monitored installation of concrete pavement, plumbing, wiring, sewers, and foundations. He also reviewed and interpreted plans and specifications for roadway, conferred with the owner to recommend actions and maintained daily logs and inspection records with photographs. |
|---------------|---|


|  |   |   |  |   |
|--|---|---|--|---|
| Firm employed by – <b>Linfield, Hunter &amp; Junius, Inc.</b>  |   |   |  |   |
| Name   | <b>Bryce L. Vazquez</b>   |   | Years of experience with this firm/employer        | 4 |
| Title  | Resident Inspector  |   | Years of experience with other firm(s)/employer(s) | 0 |
| Degree(s) / Years / Specialization   |   | University of New Orleans/ BS /Civil Engineering/2020 |  |   |
| Active registration number / state / expiration date   |   | N/A   |  |   |
| Year registered  | N/A   | Discipline  | N/A  |   |
| Contract role(s) / brief description of responsibilities   |   | Certified Inspector - Primary                         |  |   |
| Experience dates (mm/yy–mm/yy)   | Experience and qualifications relevant to the proposed contract; <i>i.e.</i> , “designed drainage”, “designed girders”, “designed intersection”, etc.   |   |  |   |
|  <b>REGISTRATIONS/CERTIFICATIONS:</b><br>LADOTD – HMA Paving Inspector/Technician<br>LADOTD – Embankment and Base Course Inspector<br>ATSSA – Certified Flagger/Traffic Control Technician/Traffic Control Supervisor |   |   |  |   |
| 04/23 – Ongoing  | <b><u>NEW ORLEANS LANDBRIDGE SHORELINE STABILIZATION AND MARSH CREATION PROJECT (CPRA), SLIDELL, LA</u></b><br>Vazquez is the Lead Inspector for this project that consists of the hydraulic dredging of three marsh creation areas including the construction of earthen containment dikes. Linfield, Hunter & Junius, Inc. is providing construction engineering and resident inspection services for this project. Vazquez coordinates resident inspection, reviews inspector daily reports, reviews contractor invoice quantities, reviews contractor certified payrolls, conducts Davis-Bacon interviews and provides resident inspection on an as-needed basis. |   |  |   |
| 04/22 – 04/23  | <b><u>VULCAN STREET DRAINAGE IMPROVEMENTS, JEFFERSON PARISH, LA</u></b><br>Vazquez was the Lead Inspector for this project that included drainage improvements along Vulcan Street between Par 3 Drive and Telestar Street including replacement of gravity sewer, replacement of concrete roadway pavement, curbing, driveways and sidewalks. Vazquez coordinated resident inspection, reviewed inspector daily reports, reviewed contractor invoices and provided resident inspection on an as-needed basis.  |   |  |   |
| 06/21 – 12/22  | <b><u>N. SIBLEY STREET AT WEST NAPOLEON SUBSURFACE DRAINAGE IMPROVEMENTS (PHASE I II) JEFFERSON PARISH, LA</u></b><br>Vazquez was the Resident Inspector for this subsurface drainage project that consisted of removing concrete walks and drives to install a new 1130 linear feet of 8” PVC/C900 Water Main, removing 1000 feet of PCC pavement to install new 24” R.C.P. drain line, and replacing 6” sewer lines with PVC on a residential street in   |   |  |   |

|               |  |
|---------------|--|
|               | Metairie, LA. Vazquez monitored the work and contractor QC and QA activities, coordinated materials testing activities, verified contractor payment request quantities and prepared daily reports summarizing construction activities.   |
| 02/21 – 06/21 | <p><b><u>FLOOD GATE REPAIRS GATES W-33 &amp; E-07 FOR SOUTH LOUISIANA FLOOD PROTECTION AUTHORITY EAST</u></b></p> <p>Vazquez was the Resident Inspector for this project that consisted of demolishing sections of broken flood gate wall and repairing the concrete embankment wall, column, and flood gate. Vazquez monitored the work and contractor QC and QA activities, recorded contractor work time and train delay time, verified contractor payment request quantities and prepared reports summarizing daily construction activities.</p> |



**16. Staff Experience:**

|   |   |   |     |
|---|---|---|-----|
| <i>Firm employed by</i>   | Michael Baker International, Inc.   |   |     |
| <i>Name</i>   | <b>Aaron Hungerford</b>   | <i>Years of relevant experience with this employer</i>  | 9   |
| <i>Title</i>  | Construction Inspector  | <i>Years of relevant experience with other employer(s)</i>  | 22  |
| <i>Degree(s) / Years / Specialization</i>   | A.S., 1994, Chemistry/Petroleum Services Technology, McNeese State University   |   |     |
| <i>Active registration number / state / expiration date</i>   | Traffic Control Supervisor / LA State Specific / exp. 08/21/2028; Certified Flagger / LA State Specific / exp. 01/22/2029; PCC Paving Inspector / LA State Specific / exp. 09/30/2029; Structural Concrete Inspector / LA State Specific / exp. 11/2/2027; Embankment & Base Inspector / LA State Specific / exp. 09/18/2027; Asphalt Paving Inspector / LA State Specific / exp. 07/15/2029  |   |     |
| <i>Year registered</i>  | N/A   | <i>Discipline</i>   | N/A |
| <i>Contract role(s) / brief description of responsibilities</i>   | Construction Inspector  |   |     |
| As a former DOTD District 03 Inspector, Aaron is highly experienced in the inspection of transportation construction projects ranging from bridge installations/replacements to roadway, intersection, and traffic signal upgrades. He is certified in the inspection of multiple construction materials types and is ready to apply nearly a decade of relevant, local experience to verify the efficient and accurate construction of this project. |   | <ul style="list-style-type: none"> <li>✓ Former District 03 Inspector leading our inspection team for this project</li> <li>✓ Fully Certified Inspector</li> <li>✓ Located nearby the project site</li> </ul> |     |
| <i>Experience dates (mm/yy-mm/yy)</i>   | <i>Experience and qualifications relevant to the proposed contract; i.e., "designed drainage", "designed girders", "designed intersection", etc. Experience dates should cover the years of experience specified in the applicable MPR(s).</i>  |   |     |
| 08/24 - Ongoing   | <b>Carpenter's Bridge Road over Whiskey Chitto Creek, Kinder, Louisiana. DOTD. Construction Inspector.</b> Aaron performed asphalt paving inspection for the asphalt binder and wearing course on this project. Work included documenting work on the Asphalt Roadway Report for upload into Headlight Material. Provided construction engineering and inspection services for this off-system bridge replacement project for Allen Parish. As the third task order under the District 03 CE&I IDIQ, the timber Carpenter Bridge over Whiskey Chitto Creek was fully removed and is being replaced with concrete simple span structure, including upgraded roadway approaches.  |   |     |
| 06/21 - 06/22   | <b>H.012099.6-LA13: 2.7 MI N LA14 - 0.2 MIN Acadia P/L, Vermilion and Acadia Parishes LA. DOTD (c/o Prairie Construction). Lead Inspector.</b> Responsible for inspection, materials sampling, testing and documentation per DOTD policies, practices and procedures including TTC, clearing and grubbing, guardrail removal and replacement with updated guardrail and end treatments, asphalt pavement patching, pavement widening, milling to grade over composite pavement, chip seal, 15,000 tons Asphaltic Concrete for Paving roadway, turnouts and drives, thermoplastic striping, mailbox removal and installation, IRI, hydro seeding. Daily documentation of contractor activities, adverse traffic conditions and pay items via Headlight and Site Manager. |   |     |
| 05/19 - 04/20   | <b>H.012081.6-LA338 at LA14 Bypass, Vermilion Parish LA. DOTD (c/o Glenn Lege Construction). Lead Inspector.</b> Responsible for inspection, materials sampling, testing and documentation per DOTD policies practices and procedures including TTC, clearing and grubbing, excavation and embankment for storm drain, catch basins, Concrete walks and drives, Class II base for PCC pavement widening, combo curb and gutter, milling to grade over composite pavement, Asphaltic Concrete, thermoplastic striping, hydro seeding, Daily documentation of contractor activities, adverse traffic conditions and pay items via Site Manager.   |   |     |
| 11/18 - 04/19   | <b>H.011789.6-LA14 BYP: Right Turn Lane at US167, Vermilion Parish LA. DOTD (c/o Siema Construction). Lead Inspector.</b> Responsible for inspection, materials sampling, testing and documentation per DOTD policies, practices and procedures including TTC, Grading drainage structures, pavement patching, Class II Base, PCC pavement and related structures. Daily documentation of contractor activities, adverse traffic conditions and pay items via Site Manager.   |   |     |



|                 |   |
|-----------------|---|
| 09/23 - Ongoing | <b>District 03 IDIQ, Task Order 2: US 90 RR-Pinhook, LA 92-LA 88. DOTD. Inspector - Lead.</b> Aaron is performing inspections on diamond grinding concrete pavement, diamond grooving concrete pavement, concrete pavement patching, asphalt overlay, dowel bar retrofitting of concrete, high density polyurethane foam "slab jacking", and other related work on US 90 and US 167 in Lafayette, St Martin and Iberia Parishes. As the lead inspector, he is also overseeing and training a certified inspector, verifying daily diaries are accurate and timely on headlight, verifying all material testing is taken documentation for closeout is obtained, and paying for work completed on the partial estimate.  |
| 12/23 - 03/24   | <b>Adaptive Traffic Signal Project, Lafayette, Louisiana. DOTD. Construction Inspector.</b> Aaron was tasked with Quality Verification for the function of Travel Safely iPhone App <i>on all 300 intersections installed under this contract.</i> As the third task order under the IDIQ "CE&I with Majority of Work in District 07 Statewide," Michael Baker is providing construction management, inspection, and administrative services for an adaptive traffic signal design and implementation project. The project involves upgrading and installing controllers and GPS-based preemption and intersection devices at 190 intersections and installing a new server at Louisiana Consolidated Government (LCG). |
| 10/20 - 11/20   | <b>Disaster Debris Removal Reduction and Disposal due to Hurricanes Laura and Delta. Parishes of Acadia, Allen, Calcasieu, Cameron, Evangeline, Iberia, Jeff Davis, Lafayette, St. Landry, St. Mary and Vermilion, LA. DOTD. Lead Inspector.</b> Responsible for supervising the contract inspection firm (Metric) and debris removal firm (TFR Enterprises) to ensure right-of-ways were cleared in a safe and efficient manner. Also worked as a liaison with Louisiana Department of Environmental Quality and Louisiana Department of Natural Resources pertaining to curtain burning and other environmental impacts.  |
| 11/23 - Ongoing | <b>H.014415.6- LA 352 Drainage Improvements. DOTD. Lead Inspector.</b> Responsible for excavation and embankment for installation of reinforced concrete box culverts, storm drainage, catch basins, concrete driveways and other related work. Oversaw and trained certified inspectors in quality assurance for daily diaries on Headlight as well as verification of all material testing is taken and documentation for closeout is obtained and insuring that paying for work completed on the partial estimate is done so in a timely manner.   |
| 06/18 - 11/18   | <b>H.002747.6- LA 335 Bridges, Vermilion Parish LA. DOTD. Certified Inspector.</b> Responsible for inspecting the removal of bridges, grading, drainage structures, milling asphalt pavement, class II base, grade control, Superpave asphaltic concrete, precast concrete pile driving, sheet pile wall driving, geotextile fabric with riprap, concrete slab span bridges, approaches and hydro seeding. Performed quality assurance for daily diaries on Headlight, as well as verification that material testing was taken and documentation for closeout was obtained.   |
| 05/17 - 06/18   | <b>H.002048.6- LA 82 Bridges, Vermilion Parish LA. DOTD. Certified Inspector.</b> Responsible for inspecting excavation and embankment for bypass bridge, H-pile driving, concrete precast slab span bridge, removal of existing bridges, grading drainage structures, milling asphalt pavement, class II base, grade control, Superpave asphaltic concrete, precast concrete pile driving, sheet pile wall driving, geotextile fabric with riprap, concrete slab span bridges, approaches and hydro seeding. Performed quality assurance for daily diaries on Headlight, as well as verification that material testing was taken and documentation for closeout was obtained.  |
| 07/22 - 09/23   | <b>H.010353.6- US167: Access Management (LFT Turn Lanes), Lafayette and Vermilion Parishes LA. DOTD. Certified Inspector.</b> Responsible for inspecting grading, drainage structures, milling asphalt pavement, asphaltic pavement patching, subgrade treatment, class II base, lime treatment, asphalt pavement widening, asphalt pavement, portland concrete paving, traffic signalization, street lighting thermoplastic striping and hydro seeding. Performed quality assurance for daily diaries on Headlight, as well as verification that material testing was taken and documentation for closeout was obtained.   |
| 05/17 - 04/18   | <b>H.005508.6- Verot School RD (Vincent - EX. 5-L), Lafayette Parish, LA. DOTD. Certified Inspector.</b> Responsible for inspecting grading, excavation and embankment for storm drains, catch basins and concrete driveways, class II base, portland concrete paving, traffic signalization, thermoplastic striping. Performed quality assurance for daily diaries on Headlight, as well as verification that material testing was taken and documentation for closeout was obtained.  |

**17. Firm Experience:**

|   |  |   |  |           |
|---|--|---|--|-----------|
| Firm name                               | <b>Linfield, Hunter &amp; Junius, Inc.</b> |   | Past Performance Evaluation Category(ies)*             | CE&I/OV   |
| Project name                            | <b>LA 352 Drainage Improvement</b>         |   | Firm responsibility (prime or sub?)                    | Sub       |
| Project number                          | H.014415                                   | Owner's name  | Louisiana Department of Transportation and Development |           |
| Project location                        | St. Martin Parish, LA                      |   | Owner's Project Manager                                | See Below |
| Owner's address, phone, email           | See Below                                  |   |  |           |
| Services commenced by this firm (mm/yy) | 10/23                                      | Total consultant contract cost (\$1,000's)                    |  | \$234     |
| Services completed by this firm (mm/yy) | Ongoing                                    | Cost of consultant services provided by this firm (\$1,000's) |  | \$167     |

Linfield, Hunter & Junius, Inc. (LH&J) is providing resident inspection services for this project that consists of the installation of approximately 1,000 linear feet of new concrete box culvert along LA 352 from LA 347 east and also subsurface drainage improvements at a roundabout along LA 347. Included in this project is grading, drainage structures, milled asphalt pavement, pavement patching, and concrete turnouts. Duties include:

- Attended the pre-construction meeting.
- Document daily activity including contractor's personnel and equipment being utilized on the project.
- Inspect the Contractor's traffic control for proper sign and barricade usage and placement.
- Inspect the Contractor's construction operations to ensure that the work is being performed in accordance with the plans and specifications.
- Maintain field records using **LADOTD's Site Manager Program/Headlight.**

The prime consultant for this contract is Michael Baker International, Inc.

Contact: Mary Flynn  
2600 CitiPlace Drive, Suite 450  
Baton Rouge, LA 70817  
225-706-0744


100% of work performed in Louisiana

**Relevant Key Features**

- ✓ DOTD Project
- ✓ Resident Inspection
- ✓ Subsurface Drainage
- ✓ PCC Pavement
- ✓ Asphaltic Concrete

**Relevant Key Personnel**


- ✓ Nathan J. Junius, P.E., P.L.S.
- ✓ Robert E. Nockton, P.E.

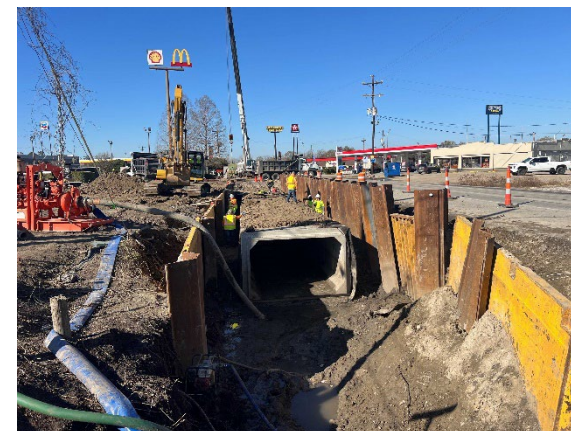



**17. Firm Experience:**

|   |   |   |  |           |
|---|---|---|--|-----------|
| Firm name                               | <b>Linfield, Hunter &amp; Junius, Inc.</b>    |   | Past Performance Evaluation Category(ies)*             | CE&I/OV   |
| Project name                            | <b>US 90: RR Jct – Pinhook, LA 92 – LA 88</b> |   | Firm responsibility (prime or sub?)                    | Sub       |
| Project number                          | H.009629                                      | Owner's name  | Louisiana Department of Transportation and Development |           |
| Project location                        | Iberia, Lafayette and St. Martin Parishes, LA |   | Owner's Project Manager                                | See Below |
| Owner's address, phone, email           | See Below                                     |   |  |           |
| Services commenced by this firm (mm/yy) | 09/23   | Total consultant contract cost (\$1,000's)                    |  | \$734     |
| Services completed by this firm (mm/yy) | Ongoing                                       | Cost of consultant services provided by this firm (\$1,000's) |  | \$372     |

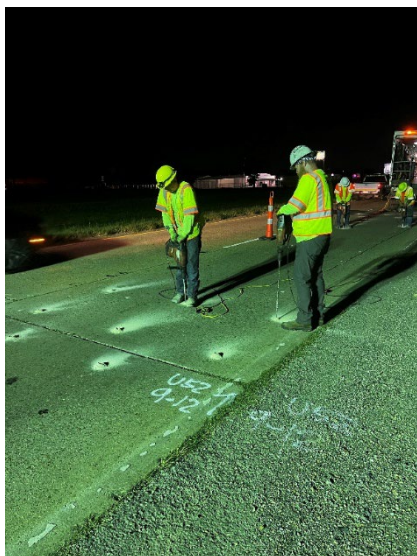

Linfield, Hunter & Junius, Inc. (LH&J) is providing resident inspection services for this project that consists of the replacement of existing concrete pavement roadway panels, milling and overlaying of asphalt shoulders, slab-jacking of existing concrete roadway panel and pavement striping along US 90/US 167 between the railroad crossing and E. Pinhook Road and along US 90 between LA 92 and LA 88. Duties include:

- Attended the pre-construction meeting.
- Document daily activity including contractor's personnel and equipment being utilized on the project.
- Inspect the Contractor's traffic control for proper sign and barricade usage and placement.
- Inspect the Contractor's construction operations (daily)

to ensure that the work is being performed in accordance with the specified plans and specifications.

- Maintain field records using **LADOTD's Site Manager Program/Headlight.**

The prime consultant for this contract is Michael Baker International, Inc.

Contact: Mary Flynn  
2600 CitiPlace Drive, Suite 450  
Baton Rouge, LA 70817  
225-706-0744


100% of work performed in Louisiana

**Relevant Key Features**

- ✓ **LADOTD Project**
- ✓ **Resident Inspection**
- ✓ **PCC Pavement**
- ✓ **Asphaltic Concrete**

**Relevant Key Personnel**

- ✓ **Nathan J. Junius, P.E., P.L.S.**
- ✓ **Robert E. Nockton, P.E.**
- ✓ **Bajazit Muminovic, E.I.**

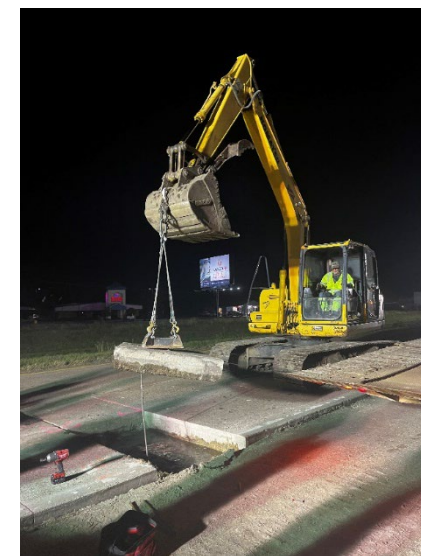



## 17. Firm Experience:

|   |   |   |  |                         |
|---|---|---|--|-------------------------|
| Firm name                               | <b>Linfield, Hunter &amp; Junius, Inc.</b>            |   | Past Performance Evaluation Category(ies)* | CE&I/OV                 |
| Project name                            | <b>Vulcan Street Drainage Improvements</b>            |   | Firm responsibility (prime or sub?)        | Prime                   |
| Project number                          | N/A   | Owner's name  | Jefferson Parish Government                |                         |
| Project location                        | Jefferson Parish, LA                                  |   | Owner's Project Manager                    | Neil D. Schneider, P.E. |
| Owner's address, phone, email           | 1221 Elmwood Park Blvd., Suite 906, Harahan, LA 70123 |   |  |                         |
| Services commenced by this firm (mm/yy) | 11/19   | Total consultant contract cost (\$1,000's)                    |  | \$221                   |
| Services completed by this firm (mm/yy) | 04/23   | Cost of consultant services provided by this firm (\$1,000's) |  | \$221                   |

This project consisted of the installation of approximately 775 linear feet of 26"x43" reinforced concrete arch drain pipe and 225 linear feet of 18"x28" reinforced concrete arch drain pipe along Vulcan Street between Par 3 Drive and Telestar Street and included the construction of seven special catch basins, relocation of approximately 700 linear feet of gravity sewer and associated site work. The new drain pipe was installed in a residential neighborhood, necessitating the complete reconstruction of approximately 1,000 linear feet of concrete roadway and curbing, adjacent driveways and portions of sidewalk.



Linfield, Hunter & Junius, Inc. provided topographic surveying services, engineering design and construction administration and engineering and resident inspection for this project.



100% of work performed in Louisiana



### Relevant Key Features

- ✓ Jefferson Parish Project
- ✓ Construction Engineering
- ✓ Resident Inspection
- ✓ Subsurface Drainage
- ✓ PCC Pavement
- ✓ Asphaltic Concrete
- ✓ Concrete Curb
- ✓ Sidewalk Replacement
- ✓ ADA Ramps
- ✓ As-Built Drawings

### Relevant Key Personnel

- ✓ Nathan J. Junius, P.E., P.L.S.
- ✓ Robert E. Nockton, P.E.
- ✓ Bryce Vazquez

**17. Firm Experience:**

|   |  |  |   |  |             |
|---|--|--|---|--|-------------|
| Firm name                               | Linfield, Hunter & Junius, Inc.                    |  |   | Past Performance Evaluation Category(ies)* | CE&I/OV     |
| Project name                            | Jefferson Parish District 5 Streets Reconstruction |  |   | Firm responsibility (prime or sub?)        | Prime       |
| Project number                          | N/A  |  | Owner's name  | Jefferson Parish Government                |             |
| Project location                        | Metairie, LA                                       |  |   | Owner's Project Manager                    | Mark Drewes |
| Owner's address, phone, email           |  | 1221 Elmwood Park Boulevard, Harahan, LA 70123 – 504-738-6833 – mdrewes@jeffparish.net |   |  |             |
| Services commenced by this firm (mm/yy) |  | 03/2006  | Total consultant contract cost (\$1,000's)                    |  | \$975       |
| Services completed by this firm (mm/yy) |  | 11/2014  | Cost of consultant services provided by this firm (\$1,000's) |  | \$975       |

This project included the milling and overlay of over 100 flood damaged streets on the East Bank of Jefferson Parish. Services provided by the firm included evaluation of the roadway, coring, cost estimating, and providing complete design services including development of design criteria, construction engineering and resident inspection.



100% of work performed in Louisiana

**Relevant Key Features**

- ✓ Jefferson Parish Project
- ✓ Construction Engineering
- ✓ Resident Inspection
- ✓ Resurfacing Existing Asphalt Pavement
- ✓ Concrete Curb Replacement
- ✓ Sidewalk Replacement
- ✓ ADA Ramps
- ✓ As-Built Drawings

**Relevant Key Personnel**

- ✓ Nathan J. Junius, P.E., P.L.S.

**17. Firm Experience:**

|   |  |   |                             |   |             |
|---|--|---|-----------------------------|---|-------------|
| Firm name                               | Linfield, Hunter & Junius, Inc.  |   |                             | Past Performance Evaluation Category (ies)* | CE&I/OV     |
| Project name                            | East and West Livingston Road Improvements   |   |                             | Firm responsibility (prime or sub?)         | Prime       |
| Project number                          | N/A  | Owner's name  | Jefferson Parish Government |   |             |
| Project location                        | Metairie, LA   |   |                             | Owner's Project Manager                     | Mark Drewes |
| Owner's address, phone, email           | 1221 Elmwood Park Boulevard, Harahan, LA 70123 – 504-738-6833 – mdrewes@jeffparish.net |   |                             |   |             |
| Services commenced by this firm (mm/yy) | 02/08  | Total consultant contract cost (\$1,000's)                    |                             |   | \$710       |
| Services completed by this firm (mm/yy) | 10/12  | Cost of consultant services provided by this firm (\$1,000's) |                             |   | \$710       |

East and West Livingston are two residential roads in Old Metairie on the East Bank of Jefferson Parish. The subsurface drainage systems in each road were substandard resulting in heavy flooding during normal intense rainstorms. The firm identified subsurface drainage improvements needed during preparation of a master drainage plan for Old Metairie developed for the Jefferson Parish Government and was subsequently retained by the Parish to provide

engineering services for reconstruction of the roadway and installation of the new subsurface drains. Project included **subsurface drainage, utility relocation and adjustment, asphalt replacement, curb replacement and sidewalk replacement.**



Services included providing topographic surveys, preparing plans, specifications and cost estimates, construction engineering and resident inspection and preparing final “as-built” drawings.

100% of work performed in Louisiana

**Key Relevant Features**

- ✓ **Jefferson Parish Project**
- ✓ **Construction Engineering**
- ✓ **Resident Inspection**
- ✓ **Asphalt Pavement**
- ✓ **Concrete Curb Replacement**
- ✓ **Sidewalk Replacement**
- ✓ **As-Built Drawings**

**Key Personnel**

- ✓ **Nathan J. Junius, P.E., P.L.S.**
- ✓ **Robert E. Nockton, P.E.**



**17. Firm Experience:**

|  |   |  |  |
|--|---|--|--|
| <i>Firm name</i>                               | Michael Baker International, Inc.   | <i>Past Performance Evaluation Discipline(s)*</i>                    | CE&I/OV  |
| <i>Project name</i>                            | <b>IDIQ Contract for CE&amp;I Services in District 61</b>                             | <i>Firm responsibility (prime or sub?)</i>                           | Prime  |
| <i>Project number</i>                          | 4400004729 (CE&I)   | <i>Owner's Name</i>  | Louisiana Department of Transportation and Development |
| <i>Project location</i>                        | Various, District 61  | <i>Owner's Project Manager</i>                                       | Josh Stutes  |
| <i>Owner's address, phone, email</i>           | 1201 Capitol Access Road, Baton Rouge, LA 70804   225-231-4103   joshua.stutes@la.gov |  |  |
| <i>Services commenced by this firm (mm/yy)</i> | 05/23   | <i>Total consultant contract cost (\$1,000's)</i>                    | \$4004.8   |
| <i>Services completed by this firm (mm/yy)</i> | Ongoing   | <i>Cost of consultant services provided by this firm (\$1,000's)</i> | \$690.4  |

The following are Task Order descriptions under the District 61 IDIQ for which Michael Baker is the prime consultant providing either full service or staff augmentation:

**FULL-SERVICE CE&I TASK ORDERS:** For these task orders, Michael Baker provided project engineering, administrative, and construction inspection services to fulfill all duties normally performed by a DOTD PE office.

**Task Order 1: H.013997 Loc Road over Borrow Pit, St James, Louisiana.** A temporary precast bridge was installed at the entrance to St. James Boat Club, the existing timber was removed, and a new simple span concrete bridge installed at the original bridge's location. Michael Baker led communication between the Boat Club Board of Directors, St. James Parish representatives and DOTD. **Complete.**

**Task Order 3: H.013458 Manchac and HH Wilson Road Bridges, Ascension Parish.** The scope of work for this task included the removal of 2 timber structures, installation of low profile detour road, installation of 2 multi barrel box culverts and subsequent base and asphalt pavement tie in to existing road. **Complete.**

**Task Order 4: H.015604 Pear Street. Assumption Parish.** The scope of work for this task included the elimination of a drainage ditch by installing double 6' diameter barrel polypropylene pipe, headwall, and cross drains. **Complete.**

**Task Order 5: H.012057 LA 431: Villar Canal and Villar Drainage Bridges, Ascension Parish.** The scope of work for this task includes the installation of a temporary detour road including 2 pipe culvert structures, removal and replacement of existing bridges, mill and asphalt overlay. **Ongoing.**

**Task Order 6: H.013956 Beamon Road Bridge, Pointe Coupee Parish.** The scope of work for this task included the removal and of one timber structure and replace with slab span concrete bridge on concrete pile, cement stabilized roadway base, asphalt pavement, coordination with parish for adjacent project. **Complete.**

**Task Order 7: H.014319 Cedarcrest Ave over Bayou, East Baton Rouge Parish.** The scope of work for this task included the removal of timber structure, insallation of multi barrel concrete box culvert, stone base, asphalt pavement. **Complete.**

**Task Order 8: H.015944 LA3125 (LA70-LA3213), St. James Parish.** The scope of work for this task included asphalt pavement patching, mill and asphalt overlay of 12 miles of highway.

**Task Order 9: H.013026 Grosse Tete ER Repair, Iberville Parish.** The scope of work for this task included emergency repair of a swing bridge structure on an intercoastal waterway. Force Account records of all work, documentation maintained, public relations meetings with parish, coordination with bridge tender. Pivot bearing repair, electrical and mechanical repair, heat straightening and painting of steel girder, concrete pier repair. **Complete.**

**STAFF AUGMENTATION TASK ORDERS:**

**Task Order 2: H.012936 LA 78 (US190-LA1), Point Coupee.** Michael Baker provided project management for asphalt certified subconsultant inspectors. **Complete.**

**Task Order 10: H.014088 US61 Intersection Improvements at LA427, Ascension Parish.** Michael Baker is providing certified inspectors for drainage, pavement and signal improvements. **Ongoing.**

**Task Order 11: H.015440 LA69, Iberville Parish.** Michael Baker is providing inspectors for concrete pavement repair, asphalt overlay and slab jacking. **Ongoing.**

Prime: Linfield, Hunter & Junius, Inc.

**PROJECT SIMILARITIES**

- CE&I Services under an IDIQ Contract
- DOTD Project
- Construction of Multiple Bridges

**17. Firm Experience:**

|  |   |  |   |
|--|---|--|---|
| <i>Firm name</i>                               | Michael Baker International, Inc.   | <i>Past Performance Evaluation Discipline(s)*</i>                    | CE&I/OV   |
| <i>Project name</i>                            | <b>IDIQ Contract for CE&amp;I Services Statewide with Majority of Work in District 03</b>   | <i>Firm responsibility (prime or sub?)</i>                           | Prime   |
| <i>Project number</i>                          | Contract No. 44-24660   | <i>Owner's Name</i>  | Louisiana Department of Transportation and Development (DOTD) |
| <i>Project location</i>                        | Various Parishes in District 03 and District 07, LA   | <i>Owner's Project Manager</i>                                       | Mark Arceneaux  |
| <i>Owner's address, phone, email</i>           | 1201 Capitol Access Road, Baton Rouge, LA 70804-9245   337-262-6103   Mark.Arceneaux@la.gov |  |   |
| <i>Services commenced by this firm (mm/yy)</i> | 06/23   | <i>Total consultant contract cost (\$1,000's)</i>                    | \$2,650.5   |
| <i>Services completed by this firm (mm/yy)</i> | Ongoing   | <i>Cost of consultant services provided by this firm (\$1,000's)</i> | \$ 2,101.5  |

Under a statewide IDIQ CE&I Contract with DOTD, Michael Baker is providing CE&I services for various bridge and roadway improvement projects in both District 03 and District 07.

**Task Order 1: Carpenter Bridge Road over Whiskey Chitto Creek:** This task order involves the removal of the old timber off-system bridge structure, and construction of a 17 span bridge on precast concrete pile, and class II stone base and asphalt pavement approaches. Michael Baker provided construction engineering and inspection services for this off-system bridge replacement project for Allen Parish.

**Task Order 2: H.014415 LA352 Drainage Project:** This task involves the installation of new dual 72" RCP drainage structures, earthwork, asphalt mill and overlay.

**Task Order 3: US 90 Railroad Pinhook from LA 92 to LA 88:** This task involved removal and replacement of cracked and degraded concrete roadway panel, leveling of the remaining panels with polyurethane foam, concrete grinding and grooving, and an asphalt overlay on over 4.6 miles of US 90 within Lafayette, St. Martin, and Iberia parishes.

**Task Order 4: Nelson Road Extension & Bridge:** This task order involves the strategic expansion of Nelson Road towards the north, connecting it to W Sallier Drive, as well as the construction of a new bridge across Bayou Contraband adjacent to the Port of Lake Charles. The bridge extends just over 1 mile and includes 13 slab spans on precast concrete pile bents, and 15 girders spans that have pile foundations and pier column supports. Additionally, this project will include an access road to the Port of Lake Charles.

**Task Order 5: I-10: Jeff Dav PL-I-49 (Open Grade Friction Course/Slab Repair):** This project includes a 37.2 mile corridor along I-10 from the Jefferson Davis Parish line to I-49. Work entails repair of the existing pavement, asphalt overlay, an open grade friction course (OGFC) overlay, and cable barrier.



*Carpenter Bridge before (left) and after (right) replacement.*



*US 90 construction operations: slab jacking (left) and asphalt*

**PROJECT SIMILARITIES**

- CE&I Services
- DOTD Project

**Team Members Who Worked on This Project:**  
Aaron Hungerford (Inspector)





**17. Firm Experience:**

|  |  |  |  |
|--|--|--|--|
| <i>Firm name</i>                               | Michael Baker International, Inc.                                      | <i>Past Performance Evaluation Discipline(s)*</i>                    | CE&I/OV  |
| <i>Project name</i>                            | <b>IDIQ: CE&amp;I with Majority of Work in District 07 Statewide</b>   | <i>Firm responsibility (prime or sub?)</i>                           | Prime  |
| <i>Project number</i>                          | Contract No. 44-14845  | <i>Owner's Name</i>  | Louisiana Department of Transportation and Development |
| <i>Project location</i>                        | Calcasieu Parish, LA   | <i>Owner's Project Manager</i>                                       | Patrick Cusey, PE                                      |
| <i>Owner's address, phone, email</i>           | 5827 Hwy 90 E., Lake Charles, LA   337-437-9115   Patrick.Cusey@la.gov |  |  |
| <i>Services commenced by this firm (mm/yy)</i> | 03/19  | <i>Total consultant contract cost (\$1,000's)</i>                    | \$3,493.87   |
| <i>Services completed by this firm (mm/yy)</i> | 03/24  | <i>Cost of consultant services provided by this firm (\$1,000's)</i> | \$2,747.6  |

Under a statewide IDIQ CE&I Contract with DOTD, Michael Baker provided Staff Augmentation Services (SAS) to augment District 07 inspection. Certified inspectors have been utilized for lead structural inspection, support roadway and drainage inspection, and support asphalt plant inspection.

**I-10: Tx State Line to East of Coone Gully:** This project involves widening 10.5 miles of I-10 to six lanes from the Texas state line to east of LA 108, replacing and widening 10 bridges, and replacing the eastbound weigh-in-motion system. This task order is for segment one of this project, from the Texas State line to LA 109.

**Michael Baker has provided two full-time inspectors** to assist in structural inspection, drainage installation, PCC paving, asphalt placement, and new asphalt plant start-up. The asphalt plant for this project is in Beaumont, TX and has never been utilized for DOTD projects. Our lead asphalt plant inspector inspected from the plant to verify all operations were running according to LADOTD standard upon startup.

Inspector duties include inspection, testing and sampling of associated work; entering daily entries in Headlight; submitting samples and tests in SiteManager Materials and LAPAVE system; maintaining documentation related to the sampling plan to ensure correct quantity of sampling, testing and documentation is maintained; providing training for LADOTD Engineering Technicians, and acceptance of work inspected.

**I-210 Prien Lake Re-Deck and Safety Improvement Project:** As the first Task Order under this IDIQ, Michael Baker provided 07 inspection and administrative staff to support District 07 with the I-210 Prien Lake superstructure deck replacement, installing safety inspection walkway, bridge barrier rail replacement, mill and overlay with asphaltic concrete, pavement striping, bridge drainage and approach slab lightening and related work. Prien Lake Bridge, also known as Israel LaFleur Bridge, is one of the highest bridges in the interstate highway system and passes over the Calcasieu Ship Channel.

Michael Baker provided a Lead Inspector who performed inspection, testing and sampling of associated work; made daily entries in the project diary (DWR); submitted samples and tests in SiteManager Materials system; maintained documentation related to the sampling plan to ensure correct quantity of sampling, testing and documentation is maintained; and provided training for DOTD Engineering Technicians and acceptance of work inspected.

Michael Baker's Field Administrator performed document control and closeout services for the DOTD Project Engineer, including AASHTOWare, Content Manager, SiteManager, SiteManager Materials, final estimate package and Form 2059 development.

**A major challenge facing DOTD was that District Project Engineer's structural staff was occupied on other projects**, which left less experienced DOTD staff on an accelerated-paced, large-scale construction project. **As a solution, Michael Baker's Lead Inspector, David Dauzat, provided on-site, hands-on training to junior DOTD staff**, drawing on lessons learned in his career. With David's support, DOTD's staff were able to seamlessly work together, prevent delays from staffing, and **deliver the project a year ahead of schedule**.

**PROJECT SIMILARITIES**

- CE&I/OV services
- DOTD Project
- Concrete inspection
- Submittal review
- Material testing



## 18. Approach and Methodology:


**Linfield, Hunter & Junius, Inc. (LH&J)**, along with **Michael Baker International, Inc. (MBI)**, have teamed together to provide a highly quality team of professionals capable of meeting the requirements of this solicitation. Throughout its fifty (50) plus year history, LH&J and predecessor firms have routinely provided quality surveying, engineering design and CE&I services for both public and private clients in Louisiana. LH&J's main office is located in central Metairie, LA and is less than 25 minutes from the project site. LH&J's team of engineers and inspectors will be supplemented by MBI to meet any project requirements.

LH&J's Project Engineer, Robert E. Nockton, P.E., has over 29 years of civil engineering experience including the CE&I for a wide range of projects. He is currently the Project Engineer for LH&J for two DOTD CE&I projects in District 03. LH&J will provide a primary certified inspector for the project, with a backup certified inspector from MBI if needed to accommodate the Contractor's work plan and schedule or if additional specialized inspections are needed.

## Project Understanding and Specific Considerations

The Linfield, Hunter & Junius, Inc. (LH&J) Team will provide Construction Contract Administration, Construction Engineering and Inspection (CE&I) services for the reconstruction of Roosevelt Boulevard from W. Napoleon Avenue to W. Metairie Avenue in Kenner, Louisiana. Construction work will include the replacement of portland cement concrete pavement reconstruction, Class II base course reconstruction and subsurface drainage installation over a total 0.56 mile project length.

Roosevelt Boulevard is a highly trafficked four lane divided thoroughfare in Kenner, Louisiana. As such, maintenance of traffic and pedestrian safety through the construction zone will be of paramount importance and will be critical to the successful completion of this project. In addition, there are numerous residences adjacent to the work and limited space for equipment and material storage. During the Pre-Construction Meeting our Team will emphasize these concerns for the Contractor to address. We will carefully review the Contractor's Traffic Control Plan as well as his plans to maintain vehicular traffic, pedestrian safety and access to adjacent residences. During construction our inspector will regularly review the Contractor's traffic control procedures to ensure they are consistent with his Traffic Control Plan.

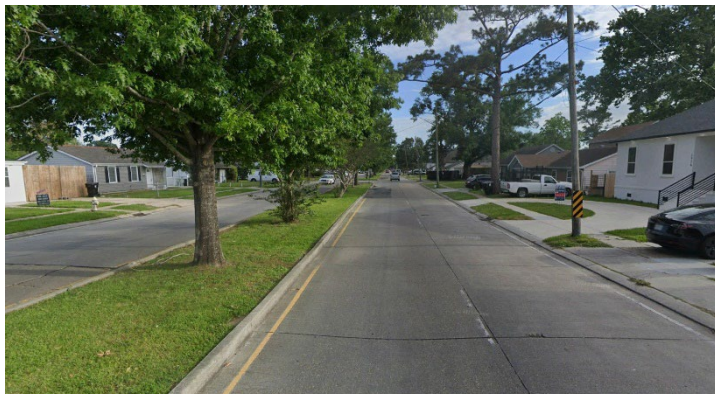

Roosevelt Boulevard near W. Metairie Avenue



Roosevelt Boulevard at 21<sup>st</sup> Street

[illegible]

## Construction Engineering & Inspection Services

Below are descriptions of the major tasks required by phase as shown in the above schedule with descriptions of work to be performed:

## Pre-Construction Phase

- **QA/QC Plan:** Within 10 days of contract award, LH&J will submit its Quality Assurance/Quality Control (QA/QC) Plan to DOTD.
- **Coordination with DOTD:** Early communication with DOTD will be critical to successful completion of this project. Our Project Engineer will communicate with the DOTD Project Engineer to review roles and responsibilities and discuss requirements of the project as well as any concerns about the project.
- **DOTD Software Access:** LH&J will set up access to SiteManager and HeadLight for all engineers and inspectors assigned to the project.
- **Review Project Documents:** LH&J will review the Construction Contract, Plans, Specifications DOTD's standard plans and special provisions to become familiar with the project goals and specific construction requirements. Also, the LH&J Inspector will perform a site visit and identify any issues that may arise during construction.

- **Pre-Construction Meeting:** The LH&J Team Project Manager (Robert Nockton) will coordinate with DOTD, the City of Kenner, the Contractor, Private Utility Representatives and other parties as appropriate to schedule and conduct a pre-construction meeting. The goal of this meeting is to relay DOTD expectations to all parties involved and to highlight any potential issues with which the Contractor needs to be aware. Discussions will include introduction of main team members, the project goals, construction schedule (including identifying a Notice to Proceed date), traffic control, pre-construction submittals and other topics outlined in the DOTD Pre-Construction Conference Checklist. An agenda and meeting minutes will be prepared and distributed to all attendees.

## **Construction Phase**

Once the Pre-Construction Meeting has been conducted, the Construction Phase will begin. Projected tasks during this phase include:

- **Construction Coordination:** The LH&J Project Engineer will coordinate construction activities with DOTD, the City of Kenner and the Contractor and will maintain continuous communication with the Inspector. This coordination is intended to maintain communication between all stakeholders from the start of construction through final acceptance. It will include conducting regular progress meetings, site visits and conducting inspections with DOTD representatives. The LH&J Project Engineer will manage all project correspondence, including submittals, RFI's, change orders and pay requests. LH&J will obtain approval from the DOTD for any changes or deviation from the construction documents.
- **Inspection:** The LH&J Inspector will perform daily inspections of construction operations to confirm that work is performed in accordance with the contract plans, specifications and approved submittals. Work items to be inspected will include, but are not limited to, drainage, base course and pavement work. Inspectors will inspect erosion control devices for conformance with DOTD Standard Plans and traffic control signs and devices for conformance with the approved Traffic Control Plan, DOTD Standard Plans and MUTCD. During inspections, extensive photographs will be taken to illustrate site conditions and to document the progress of construction activities.
- **Daily Records and Reports:** The LH&J Inspector will prepare detailed daily construction field records describing the Contractor's personnel, equipment and completed construction activities. He will also maintain clear records of quantities installed and accepted to facilitate monthly payment request reviews. All Daily Records and Reports will be prepared using HeadLight and uploaded into SiteManager.
- **Materials Sampling and Testing:** The LH&J Inspector will obtain samples and submit them to the DOTD District 02 Testing Laboratory for testing. In the event that the DOTD's testing laboratory is unavailable, tests will be performed by a qualified independent testing laboratory in accordance with the applicable DOTD testing procedures and as required by the Specifications. The LH&J Project Engineer and Inspector will review all testing reports and evaluate conformance to the Plans and Specifications. DOTD and the City of Kenner will be notified immediately of work does not conform to the Plans and Specifications.
- **Submittals, Requests for Information (RFIs) and Change Orders:** The LH&J Project Engineer will review all submittals for conformance to the requirements of the Specifications. All RFIs and Change Order requests will be reviewed in consultation with DOTD

with responses distributed to all parties. LH&J will maintain a log of Submittals, RFIs and Change Orders that includes date submitted, description and date returned.

- **Monthly Payment Requests:** The LH&J Project Engineer and Inspector will review monthly payment request quantities for conformance with the Specifications and consistency with the actual quantities documented to be complete and accepted.
- **Field Changes:** The LH&J Team will coordinate all field changes with DOTD, the City of Kenner and the Contractor. Detailed records of all field changes will be maintained including redlines to the Plans to document the nature of such changes.

### **Post-Construction Phase**

Upon notification of Substantial Completion by the Contractor, the Post-Construction Phase of the project will begin. Tasks and milestones of the Post-Construction Phase include:

- **Final Inspection:** Upon substantial completion, our team will conduct a final walk-through site visit with representatives of DOTD, the City of Kenner and the Contractor and develop punch list items for the Contractor to satisfactorily address before final acceptance of the project. Punch list items will identify work that is deficient and/or incomplete.
- **Acceptance:** Once all punch list items have been satisfactorily addressed, the Project Engineer will issue the Contractor a notice of final project acceptance.
- **Final Estimate Packages:** Following final acceptance, LH&J will prepare final estimate packages, including Form 2059 and all backup in accordance with the DOTD Construction Manual.
- **As-Built Drawings:** LH&J will develop “As-Built” plans that document the actual work performed, clearly noting all changes from the original plans due to field changes and change orders. These plans will be submitted with the final payment request.

### **Summary**

The LH&J Team has a long history of providing quality engineering services to a variety of clients, from project conception through construction. Our Team was selected to provide professionals in their respective fields who understand the scope of work and perform with a commitment to detail and responsiveness to the specific needs of the project. We respectfully request your consideration.



**19. Workload:**

| Firm(s)                           | Past Performance Evaluation Discipline(s) * | State project number  | Project name  | Remaining Unpaid Balance** |
|-----------------------------------|---|---|---|----------------------------|
| Linfield, Hunter & Junius, Inc.   | Bridge, Survey                              | STATE PROJECT NO. H.015338<br>F.A.P. NO. H015338                                | IIJA-OFF-SYSTEM BRIDGE PROGRAM DISTRICT 07 NO. 192074   | \$50,000                   |
| Linfield, Hunter & Junius, Inc.   | Bridge, Survey                              | STATE PROJECT NO. H.015493<br>F.A.P. NO. H015493                                | IIJA-OFF-SYSTEM BRIDGE PROGRAM DISTRICT 07 NO. 192074   | \$25,000                   |
| Linfield, Hunter & Junius, Inc.   | Bridge, Survey                              | STATE PROJECT NO. H.015494<br>F.A.P. NO. H015494                                | IIJA-OFF-SYSTEM BRIDGE PROGRAM DISTRICT 07 NO. 192074   | \$25,000                   |
| Linfield, Hunter & Junius, Inc.   | Bridge, Survey                              | STATE PROJECT NO. H.01495<br>F.A.P. NO. H015494                                 | IIJA-OFF-SYSTEM BRIDGE PROGRAM DISTRICT 07 NO. 192074   | \$50,000                   |
| Linfield, Hunter & Junius, Inc.   | CE&I/OV                                     | STATE CONTRACT NO. 44-24660<br>Task Order No. H.014415.6<br>S.P. No. H.014415.6 | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>LA 352 Drainage Improvement   | \$165,700                  |
|                                   |   | STATE CONTRACT NO. 44-24660<br>TASK ORDER NO. H009629.6<br>S.P.H.009629.6       | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>US 90 RR-Pinhook_ LA 92-LA 88 | \$359,466                  |
| Michael Baker International, Inc. | Road  | Contract No. 4400021519<br>S.P. No. H.012030.5<br>F.A.P. No. H012030            | US 371: KCS RR Overpasses HBI   | \$215,372                  |
|                                   | Bridge                                      | Contract No. 4400025026<br>S.P. No. H.015338<br>F.A.P. No. H015338              |   | \$488,556                  |

| Firm(s)                           | Past Performance Evaluation Discipline(s) * | State project number   | Project name  | Remaining Unpaid Balance** |
|-----------------------------------|---|--|---|----------------------------|
|                                   | Bridge                                      |  | Infrastructure Investment and Jobs Act (IIJA) Off-System Bridge Program – District 07, Supplemental Agreement No. 1                             |                            |
|                                   | Road  | Contract No. 4400019379  | LA 30: EBR PL-I-10  | \$309,475                  |
|                                   | Bridge                                      | S.P. No. H.013797  |   |                            |
|                                   | Environmental                               | F.A.P. No. H013797   |   |                            |
|                                   | Environmental                               | Contract No. 4400005484<br>S.P. No. H.005168<br>F.A.P. No. DE-9208 (500)               | NORG EIS, New Orleans, Louisiana  | \$349,225                  |
|                                   | Environmental                               | Contract No. 4400005484<br>S.P. No. H.005168   | NORG – Avondale PEL Study, New Orleans, Louisiana Supplemental Agreement  | \$339,573                  |
|                                   | Other (Water Resource)                      | Contract No. 4400017092<br>Task Order No. 4  | Collection of Existing Watershed Datasets, Models, and Studies; and Proposition of Modeling Design Approach, Schedule and Costs, Region 6       | \$1,000,000                |
|                                   | Other (Aviation)                            | Contract No. 4400019130<br>Task Order No. 1  | IDIQ Contract for Statewide Aviation Program Update – Phase II Statewide  | N/A                        |
|                                   | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 1<br>S.P. No. H.013997<br>F.A.P. No. H013997 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Loc Rd. over Borrow Pit (Blind RV BT LNCH), St. James Parish | \$98,868                   |
|                                   | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 2<br>S.P. No. H.012936<br>F.A.P. No. H012936 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, LA 78: US 190- LA 1  | \$2,787                    |
|                                   | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 3<br>S.P. No. H.013458<br>F.A.P. No. H013458 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Manchac Acres & HH Wilson Rd Bridges                         | \$9,911                    |
| Michael Baker International, Inc. | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 4<br>S.P. No. H.015604<br>F.A.P. No. H015604 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Pear St. at LA 1: Drainage                                   | \$162,004                  |



| Firm(s) | Past Performance Evaluation Discipline(s) * | State project number   | Project name  | Remaining Unpaid Balance** |
|---------|---|--|---|----------------------------|
|         | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 5<br>S.P. No. H.012057<br>F.A.P. No. H012057     | IDIQ Contract for Construction Engineering and Inspection Services in District 61, LA 431: Villar Canal and Drainage Bridges                                | \$734,079                  |
|         | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 6<br>S.P. No. H.013956<br>F.A.P. No. H013956     | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Beamon Rd over Bayou Maringouin  | \$20,821                   |
|         | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 7<br>S.P. No. H.014319<br>F.A.P. No. H014319     | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Ceadercrest Avenue over Wiener Creek                                     | \$141,738                  |
|         | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 8<br>S.P. No. H.015944<br>F.A.P. No. H015944     | IDIQ Contract for Construction Engineering and Inspection Services in District 61, LA 70 – LA 3213  | \$534,837                  |
|         | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 9<br>S.P. No. H.016026<br>F.A.P. No. H.016026    | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Grosse Tete Emergency Project  | \$380,720                  |
|         | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 10<br>S.P. No. H.014088.6<br>F.A.P. No. H.014088 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, US 61: INT. Improvements at LA 427                                       | \$336,795                  |
|         | CE&I/OV                                     | Contract No. 4400024660<br>Task Order No. 1<br>H.013958.6<br>S.P. No. H.013958.6           | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03 Carpenter Bridge Rd over Whisky Chitto Creek | \$244,374                  |
|         | CE&I/OV                                     | Contract No. 4400024660<br>Task Order No. 2<br>H.014415.6<br>S.P. No. H.014415.6           | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>LA 352 Drainage Improvement               | \$189,157                  |

| Firm(s)                           | Past Performance Evaluation Discipline(s) * | State project number  | Project name   | Remaining Unpaid Balance** |
|-----------------------------------|---|---|--|----------------------------|
| Michael Baker International, Inc. | CE&I/OV                                     | Contract No. 4400024660<br>Task Order No. 3<br>H.009629.6<br>S.P. No. H.009629.6      | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>US 90 RR-Pinhook LA 92-LA 88             | \$462,165                  |
|                                   | CE&I/OV                                     | Contract No. 4400024660<br>Task Order No. 4<br>S.P. No. H.005967.6<br>F.A.P. H.005967 | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>Nelson Rd Ext & Bridge                   | \$523,709                  |
|                                   | CE&I/OV                                     | Contract No. 4400024660<br>Task Order No. 5<br>S.P. No. H.005967.6<br>F.A.P. H.005967 | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>I-10: JEFF DAV PL-I-49(OGFC/SLAB REPAIR) | \$492,896                  |
| Michael Baker International, Inc. | Road/Bridge                                 | Contract No. 4400021519<br>S.P. No. H.012030.5<br>F.A.P. No. H012030                  | US 371: KCS RR Overpasses HBI  | \$235,961                  |
|                                   |   | Contract No. 4400025026<br>S.P. No. H.015338<br>F.A.P. No. H015338                    | Infrastructure Investment and Jobs Act (IIJA) Off-System Bridge Program – District 07, Supplemental Agreement No. 1  | \$1,002,358                |
| Michael Baker International, Inc. | Road/Bridge/ Environmental                  | Contract No. 4400019379<br>S.P. No. H.013797<br>F.A.P. No. H013797                    | LA 30: EBR PL-I-10   | \$309,268                  |
| Michael Baker International, Inc. | Environmental                               | Contract No. 4400005484<br>S.P. No. H.005168<br>F.A.P. No. DE-9208 (500)              | NORG EIS, New Orleans, Louisiana   | \$431,946                  |
| Michael Baker International, Inc. | Environmental/ Road                         | Contract No. 4400005484<br>S.P. No. H.005168  | NORG – Avondale PEL Study, New Orleans, Louisiana Supplemental Agreement   | \$546,292                  |
| Michael Baker International, Inc. | Other (Water Resource)                      | Contract No. 4400017092<br>Task Order No. 3   | Collection of Existing Watershed Datasets, Models, and Studies; and Proposition of Modeling Design Approach, Schedule and Costs, Region 6                  | \$326,742                  |

| Firm(s)                           | Past Performance Evaluation Discipline(s) * | State project number   | Project name  | Remaining Unpaid Balance** |
|-----------------------------------|---|--|---|----------------------------|
|                                   |   | Contract No. 4400017090<br>Task Order No. 2  | Collection of Existing Watershed Datasets, Models, and Studies; and<br>Proposition of Modeling Design Approach, Schedule and Costs, Region 4            | \$ 81,608                  |
|                                   |   | Contract No. 4400017067<br>Task Order No. 1  | Collection of Existing Watershed Datasets, Models, and Studies; and<br>Proposition of Modeling Design Approach, Schedule and Costs, Region 1            | \$170,387                  |
|                                   |   | Contract No. 4400023101<br>Task Order No. 1<br>S.P. No. H.015040.1&<br>H.015041.1      | IDIQ Contract for Louisiana Watershed Initiative/ State Projects Program (LWI-SPP) – Group 1<br>Beauregard, Vernon, and St. Landry Parishes             | \$31,686                   |
|                                   |   | Contract No. 4400023101<br>Task Order No. 2<br>S.P. No. H.015044.1                     | IDIQ Contract for Louisiana Watershed Initiative/ State Projects Program (LWI-SPP) – Group 1<br>Beauregard, Vernon, and St. Landry Parishes             | \$23,565                   |
|                                   |   | Contract No. 4400023101<br>Task Order No. 3<br>S.P. No. H.015047.1                     | IDIQ Contract for Louisiana Watershed Initiative/ State Projects Program (LWI-SPP) – Group 1<br>Beauregard, Vernon, and St. Landry Parishes             | \$76,002                   |
|                                   |   | Contract No. 4400023101<br>Task Order No. 4<br>S.P. No. (SEVERAL)                      | IDIQ Contract for Louisiana Watershed Initiative/ State Projects Program (LWI-SPP) – Group 1<br>Beauregard, Vernon, and St. Landry Parishes PEER REVIEW | \$10,380                   |
| Michael Baker International, Inc. | Other (Aviation)                            | Contract No. 4400019130<br>Task Order No. 1  | IDIQ Contract for Statewide Aviation Program Update – Phase II Statewide  | \$4,980                    |
| Michael Baker International, Inc. | CE&I/OV                                     | Contract No. 4400025536<br>Task Order No. 1<br>S.P. No. H.013997<br>F.A.P. No. H013997 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Loc Rd. over Borrow Pit (Blind RV BT LNCH), St. James Parish         | \$73,199                   |
|                                   |   | Contract No. 4400025536<br>Task Order No. 2<br>S.P. No. H.012936<br>F.A.P. No. H012936 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, LA 78: US 190- LA 1  | \$13,902                   |

| Firm(s)                           | Past Performance Evaluation Discipline(s) * | State project number   | Project name  | Remaining Unpaid Balance** |
|-----------------------------------|---|--|---|----------------------------|
|                                   |   | Contract No. 4400025536<br>Task Order No. 3<br>S.P. No. H.013458<br>F.A.P. No. H013458 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Manchac Acres & HH Wilson Rd Bridges   | \$115,099                  |
|                                   |   | Contract No. 4400025536<br>Task Order No. 4<br>S.P. No. H.015604<br>F.A.P. No. H015604 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Pear St. at LA 1: Drainage   | \$141,047                  |
|                                   |   | Contract No. 4400025536<br>Task Order No. 5<br>S.P. No. H.012057<br>F.A.P. No. H012057 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, LA 431: Villar Canal and Drainage Bridges  | \$734,168                  |
|                                   |   | Contract No. 4400025536<br>Task Order No. 6<br>S.P. No. H.013956<br>F.A.P. No. H013956 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Beamon Rd over Bayou Maringouin  | \$128,744                  |
|                                   |   | Contract No. 4400025536<br>Task Order No. 7<br>S.P. No. H.014319<br>F.A.P. No. H014319 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, Ceadercrest Avenue over Wiener Creek   | \$160,744                  |
|                                   |   | Contract No. 4400025536<br>Task Order No. 8<br>S.P. No. H.015944<br>F.A.P. No. H015944 | IDIQ Contract for Construction Engineering and Inspection Services in District 61, LA 70 – LA 3213  | \$655,277                  |
| Michael Baker International, Inc. | CE&I/OV                                     | Contract No. 4400014845<br>S.P. No. H.012018.6<br>F.A.P. No. H012018                   | IDIQ Contract for Construction Engineering and Inspection Services with majority of work in District 07 Statewide –Adaptive Traffic Signal and Implementation, Lafayette Parish | \$2,664                    |
|                                   |   | Contract No. 440001485<br>H.0003184.6<br>S.P. No. H.003184.6                           | IDIQ Contract for Construction Engineering and Inspection Services with majority of work in District 07 Statewide, I-10: Texas State Line - E. of Coone Gully, Calcasieu Parish | \$56,556                   |




| Firm(s) | Past Performance Evaluation Discipline(s) * | State project number  | Project name   | Remaining Unpaid Balance** |
|---------|---|---|--|----------------------------|
|         |   | Contract No. 440001485<br>S.P. No. H.013959.6<br>F.A.P. No. H013959                   | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 07 Statewide Reeds Bridge Road over Calcasieu River Relief, Calcasieu Parish | \$12,716                   |
|         |   | Contract No. 4400024660<br>Task Order No. 1<br>H.013958.6<br>S.P. No. H.013958.6      | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>Carpenter Bridge Rd over Whisky Chitto Creek                           | \$103,638                  |
|         |   | Contract No. 4400024660<br>Task Order No. 2<br>H.014415.6<br>S.P. No. H.014415.6      | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>LA 352 Drainage Improvement  | \$44,932                   |
|         |   | Contract No. 4400024660<br>Task Order No. 3<br>H.009629.6<br>S.P. No. H.009629.6      | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>US 90 RR-Pinhook LA 92-LA 88   | \$223,996                  |
|         |   | Contract No. 4400024660<br>Task Order No. 4<br>S.P. No. H.005967.6<br>F.A.P. H.005967 | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>Nelson Rd Ext & Bridge   | \$444,440                  |
|         |   | Contract No. 4400024660<br>Task Order No. 5<br>S.P. No. H.005967.6<br>F.A.P. H.005967 | IDIQ Contract for Construction Engineering and Inspection Services (CE&I) with Majority of Work in District 03<br>I-10: JEFF DAV PL-I-49(OGFC/SLAB REPAIR)                               | \$412,864                  |

(Add rows as needed)

DO NOT SUM

**20. Certifications/Licenses:**


If the advertisement requires submission of licenses and/or certificates, include them here. Otherwise, leave this section blank.

| <p><b>Linfield, Hunter &amp; Junius, Inc.</b></p> <p>The Louisiana Professional Engineering and Land Surveying Board has the following information on file:</p> <p>Name: Public Address:<br/>         3608 18th Street, Suite 200<br/>         Linfield, Hunter &amp; Junius, Inc.<br/>         Metairie, Louisiana 70002</p> <p>License/Certificate Information w/ Supervision</p> <table border="1"> <thead> <tr> <th>License</th> <th>Status</th> <th>First Issuance Date</th> <th>Expiration Date</th> <th>Supervisor(s)</th> </tr> </thead> <tbody> <tr> <td>EF.0000510</td> <td>Active</td> <td>05/23/1979</td> <td>03/31/2025</td> <td>Mr. Ralph William Junius Jr. # PE.0016053</td> </tr> </tbody> </table> | License   | Status   | First Issuance Date | Expiration Date                               | Supervisor(s) | EF.0000510 | Active | 05/23/1979 | 03/31/2025 | Mr. Ralph William Junius Jr. # PE.0016053 | <p>The Louisiana Professional Engineering and Land Surveying Board has the following information on file:</p> <p>Name: Public Address:<br/>         3608 18th Street, Suite 200<br/>         Linfield, Hunter &amp; Junius, Inc.<br/>         Metairie, Louisiana 70002</p> <p>License/Certificate Information w/ Supervision</p> <table border="1"> <thead> <tr> <th>License</th> <th>Status</th> <th>First Issuance Date</th> <th>Expiration Date</th> <th>Supervisor(s)</th> </tr> </thead> <tbody> <tr> <td>VE.0000532</td> <td>Active</td> <td>06/15/2004</td> <td>09/30/2024</td> <td>Mr. Nathan John Junius # PLS.0004958 - Active</td> </tr> </tbody> </table> | License | Status | First Issuance Date | Expiration Date | Supervisor(s) | VE.0000532 | Active | 06/15/2004 | 09/30/2024 | Mr. Nathan John Junius # PLS.0004958 - Active |  |
|--|---|--|---------------------|---|---------------|------------|--------|------------|------------|---|--|---------|--------|---------------------|-----------------|---------------|------------|--------|------------|------------|---|---|
| License  | Status  | First Issuance Date  | Expiration Date     | Supervisor(s)                                 |               |            |        |            |            |   |  |         |        |                     |                 |               |            |        |            |            |   |   |
| EF.0000510   | Active  | 05/23/1979   | 03/31/2025          | Mr. Ralph William Junius Jr. # PE.0016053     |               |            |        |            |            |   |  |         |        |                     |                 |               |            |        |            |            |   |   |
| License  | Status  | First Issuance Date  | Expiration Date     | Supervisor(s)                                 |               |            |        |            |            |   |  |         |        |                     |                 |               |            |        |            |            |   |   |
| VE.0000532   | Active  | 06/15/2004   | 09/30/2024          | Mr. Nathan John Junius # PLS.0004958 - Active |               |            |        |            |            |   |  |         |        |                     |                 |               |            |        |            |            |   |   |
|    |  |  |                     |   |               |            |        |            |            |   |  |         |        |                     |                 |               |            |        |            |            |   |   |



|  |   |  |
|--|---|--|
|  <p><b>PROOF OF TRAINING</b><br/>THIS CERTIFICATE HEREBY RECOGNIZES THAT</p> <p><b>Robert Nockton</b><br/>has attended<br/><b>Traffic Control Supervisor-LA State Specific</b><br/>Training Course</p> <p>9/6/2021 to 5/7/2025<br/>Training Valid Through</p> <p>Metairie, LA<br/>Location</p> <p><i>Robert Nockton</i><br/>Director of Training<br/><i>John Truitt</i><br/>President, CEO</p> <p><small>ATSSA provides training and certification for neither constitutes employment by ATSSA.</small></p>  |  <p><b>PROOF OF TRAINING</b><br/>THIS CERTIFICATE HEREBY RECOGNIZES THAT</p> <p><b>Robert Nockton</b><br/>has attended<br/><b>Traffic Control Technician-LA State Specific</b><br/>Training Course</p> <p>5/5/2021 to 5/5/2025<br/>Training Valid Through</p> <p>Metairie, LA<br/>Location</p> <p><i>Robert Nockton</i><br/>Director of Training<br/><i>John Truitt</i><br/>President, CEO</p> <p><small>ATSSA provides training and certification for neither constitutes employment by ATSSA.</small></p>  |  <p><b>AMERICAN TRAFFIC SAFETY SERVICES ASSOCIATION</b></p> <p><i>This is to affirm that</i><br/><b>Robert Nockton</b></p> <p><i>has satisfied the requirements to be designated as a</i><br/><b>CERTIFIED FLAGGER</b></p> <p>Expiration Date <u>5/2/2025</u> State Issued in <u>LA</u></p> <p><i>Instructor Signature</i><br/><i>Robert Nockton</i></p> <p><small>Verification available by calling 1-877-642-4637 or at <a href="http://www.flagger.com">http://www.flagger.com</a></small></p> |
|  <p><b>PROOF OF TRAINING</b><br/>THIS CERTIFICATE HEREBY RECOGNIZES THAT</p> <p><b>Bryce Vazquez</b><br/>has attended<br/><b>Traffic Control Supervisor-LA State Specific</b><br/>Training Course</p> <p>9/6/2021 to 5/7/2025<br/>Training Valid Through</p> <p>Metairie, LA<br/>Location</p> <p><i>Bryce Vazquez</i><br/>Director of Training<br/><i>John Truitt</i><br/>President, CEO</p> <p><small>ATSSA provides training and certification for neither constitutes employment by ATSSA.</small></p>    |  <p><b>PROOF OF TRAINING</b><br/>THIS CERTIFICATE HEREBY RECOGNIZES THAT</p> <p><b>Bryce Vazquez</b><br/>has attended<br/><b>Traffic Control Technician-LA State Specific</b><br/>Training Course</p> <p>5/5/2021 to 5/5/2025<br/>Training Valid Through</p> <p>Metairie, LA<br/>Location</p> <p><i>Bryce Vazquez</i><br/>Director of Training<br/><i>John Truitt</i><br/>President, CEO</p> <p><small>ATSSA provides training and certification for neither constitutes employment by ATSSA.</small></p>    |  <p><b>AMERICAN TRAFFIC SAFETY SERVICES ASSOCIATION</b></p> <p><i>This is to affirm that</i><br/><b>Bryce Vazquez</b></p> <p><i>has satisfied the requirements to be designated as a</i><br/><b>CERTIFIED FLAGGER</b></p> <p>Expiration Date <u>5/6/2025</u> State Issued in <u>LA</u></p> <p><i>Instructor Signature</i><br/><i>Bryce Vazquez</i></p> <p><small>Verification available by calling 1-877-642-4637 or at <a href="http://www.flagger.com">http://www.flagger.com</a></small></p>   |
| <p><b>State of Louisiana</b><br/><b>Department of Transportation and Development</b></p>  <p><b>Bryce Vazquez</b><br/>has met the requirements for certification as a(n):<br/><b>HMA Paving</b><br/><b>Inspector/Technician</b></p> <p><b>02 ND</b> <b>Expiration Date: 9/6/2028</b></p>   | <p><b>State of Louisiana</b><br/><b>Department of Transportation and Development</b></p>  <p><b>Bryce Vazquez</b><br/>has met the requirements for certification as a(n):<br/><b>Embankment and Base</b><br/><b>Course Inspector</b></p> <p><b>02 ND</b> <b>Expiration Date: 11/5/2029</b></p>  |  |
|  |   |  |
|  |   |  |



**Michael Baker International, Inc.**

The Louisiana Professional Engineering and Land Surveying Board has the following information on file:

| Name:                             | Public Address:  |
|-----------------------------------|--|
| Michael Baker International, Inc. | 500 Grant Street, Suite 5400<br>Pittsburgh, Pennsylvania 15219 |

**License/Certificate Information w/ Supervision**

| License    | Status | First Issuance Date | Expiration Date | Supervisor(s)   |
|------------|--------|---------------------|-----------------|---|
| EF.0000062 | Active | 09/11/1984          | 09/30/2025      | Mrs. Mary Elizabeth Flynn # PE.0036931 ; Mr. Daniel Thomas Thornhill # PE.0032367 |

**21. QA/QC Plan:**

If the advertisement requires submission of a QA/QC plan, include it here. **Otherwise, leave this section blank. If a QA/QC plan is included in this section and was not required by the advertisement, it will be redacted.**

**22. Sub-consultant information:**

If one or more sub-consultants will be used, provide the name, address, point of contact and phone number for each. Otherwise, leave this section blank.

| <b>Firm Name</b><br><b>(Name must match as registered with</b><br><b>Louisiana's Secretary of State)</b> | <b>Address</b>   | <b>Point of Contact and email address</b>   | <b>Phone Number</b> |
|--|--|---|---------------------|
| Michael Baker International, Inc.  | 2600 Citiplace Drive, Suite 450<br>Baton Rouge, LA 70808 | Mary E. Flynn, P.E.<br><a href="mailto:Mary.Flynn@mbakerintl.com">Mary.Flynn@mbakerintl.com</a> | 850-570-8969        |
|  |  |   |                     |
|  |  |   |                     |

(Add rows as needed)

**Any information included in this section will be redacted if not required by the advertisement.**

**23. Location:**

If location is an evaluation criterion for this advertisement and the prime consultant intends to establish a local presence, describe the plan for doing so. **Otherwise, leave this section blank. Any information included in this section will be redacted if not required by the advertisement.**
